

**2021 BOND PROGRAM
CONSTRUCTION UPDATE**

**GALESBURG-AUGUSTA COMMUNITY SCHOOLS
PRIMARY ADDITION & REMODEL
STADIUM & ENTRANCE BUILDINGS
HIGH SCHOOL MULTI-PURPOSE ADDITION**



6/9/2023



STADIUM OVERVIEW




COMING AUGUST OF 2023

STADIUM CONCESSIONS OVERVIEW




- Continuing brick veneer. 70% complete.
- Roof framing & blocking ongoing. 90% complete.
- Roofing ongoing 30% complete

STADIUM SITE WORK OVERVIEW

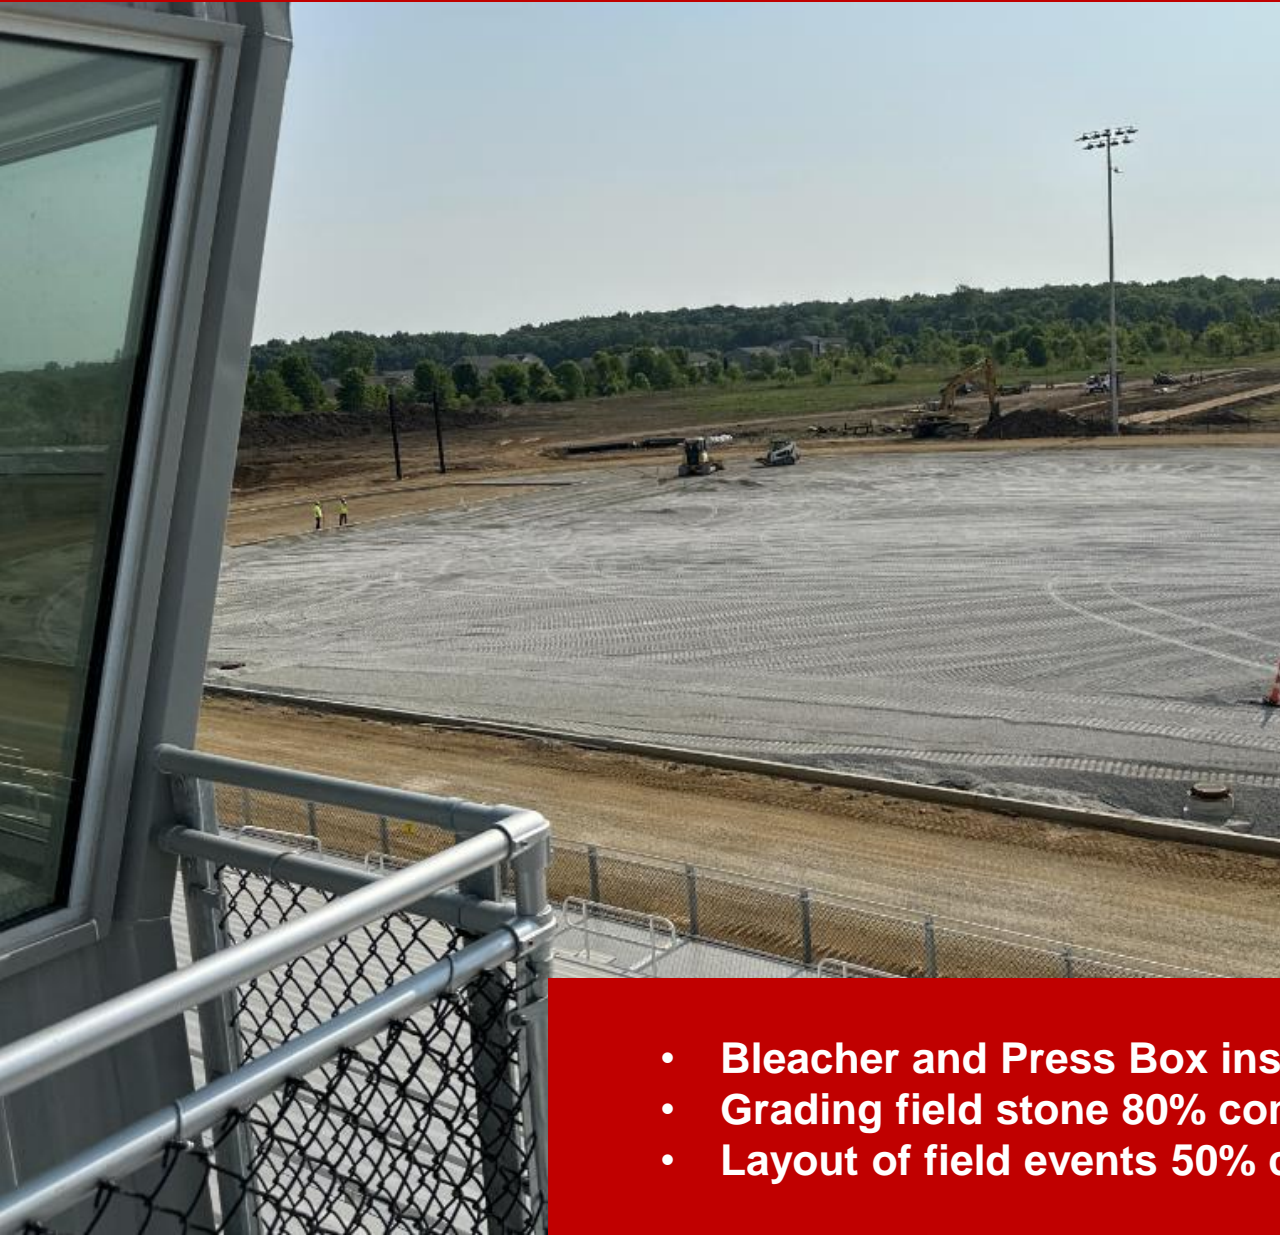

- Bleacher and Press Box install complete
- Grading field stone 80% complete
- Layout of field events 50% complete

STADIUM SITE WORK OVERVIEW

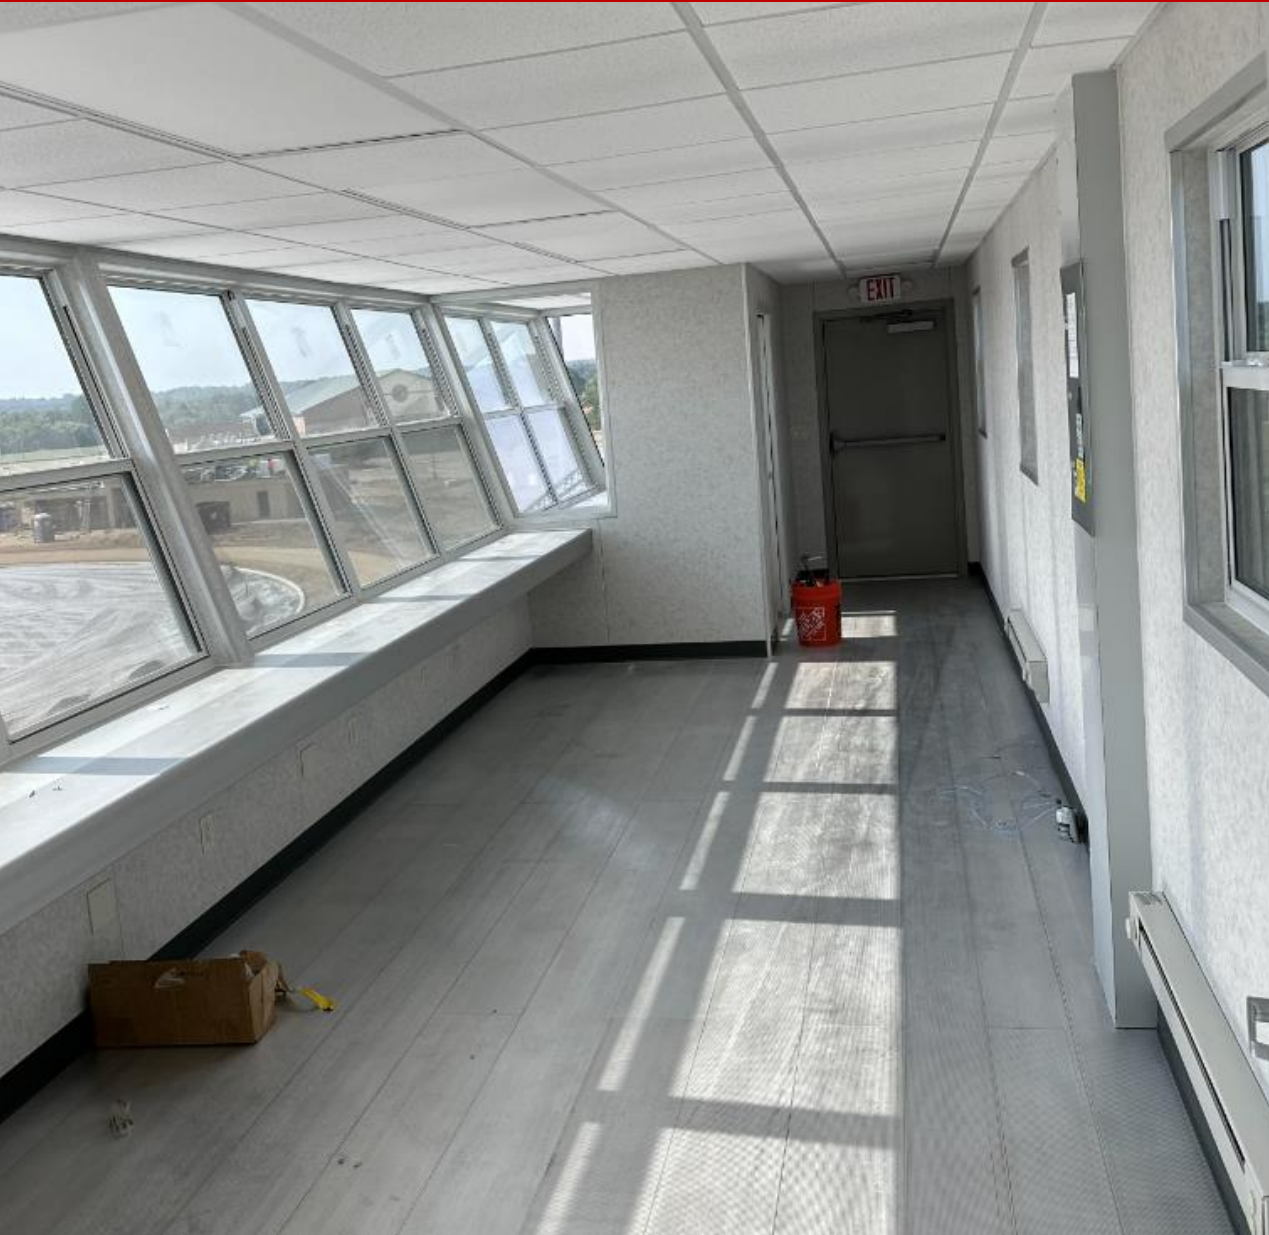

PRIMARY SITE WORK OVERVIEW



- Brick 80% complete. Finishing northern side of building
- Unit D roofing ongoing 50% complete
- Prepping for exterior windows and facia

PRIMARY SITE WORK OVERVIEW



- Students showing their appreciation on the last week of school
- Overhead electrical, mechanical & plumbing 65% complete
- Completing all interior walls and door frames

TWO WEEK LOOK AHEAD



Primary Building

- ▶ Complete brick veneer.
- ▶ Complete membrane roofing and roof blocking.
- ▶ Install exterior aluminum windows
- ▶ Begin ceiling grid and first coat of paint

Stadium & Entrance Buildings

- ▶ Complete membrane roofing and begin metal panel install at concessions building
- ▶ Complete brick veneer at concession and restroom buildings.
- ▶ Pour concrete for track and field events
- ▶ Hook up power and data to Press Box
