

**2021 BOND PROGRAM  
CONSTRUCTION UPDATE**

---

**GALESBURG-AUGUSTA COMMUNITY SCHOOLS  
PRIMARY ADDITION & REMODEL  
STADIUM & ENTRANCE BUILDINGS  
HIGH SCHOOL MULTI-PURPOSE ADDITION**



**7/14/2023**





# STADIUM SITE WORK OVERVIEW







# STADIUM SITE WORK OVERVIEW



- Completing concrete maintenance strip and fence posts



# STADIUM SITE WORK OVERVIEW

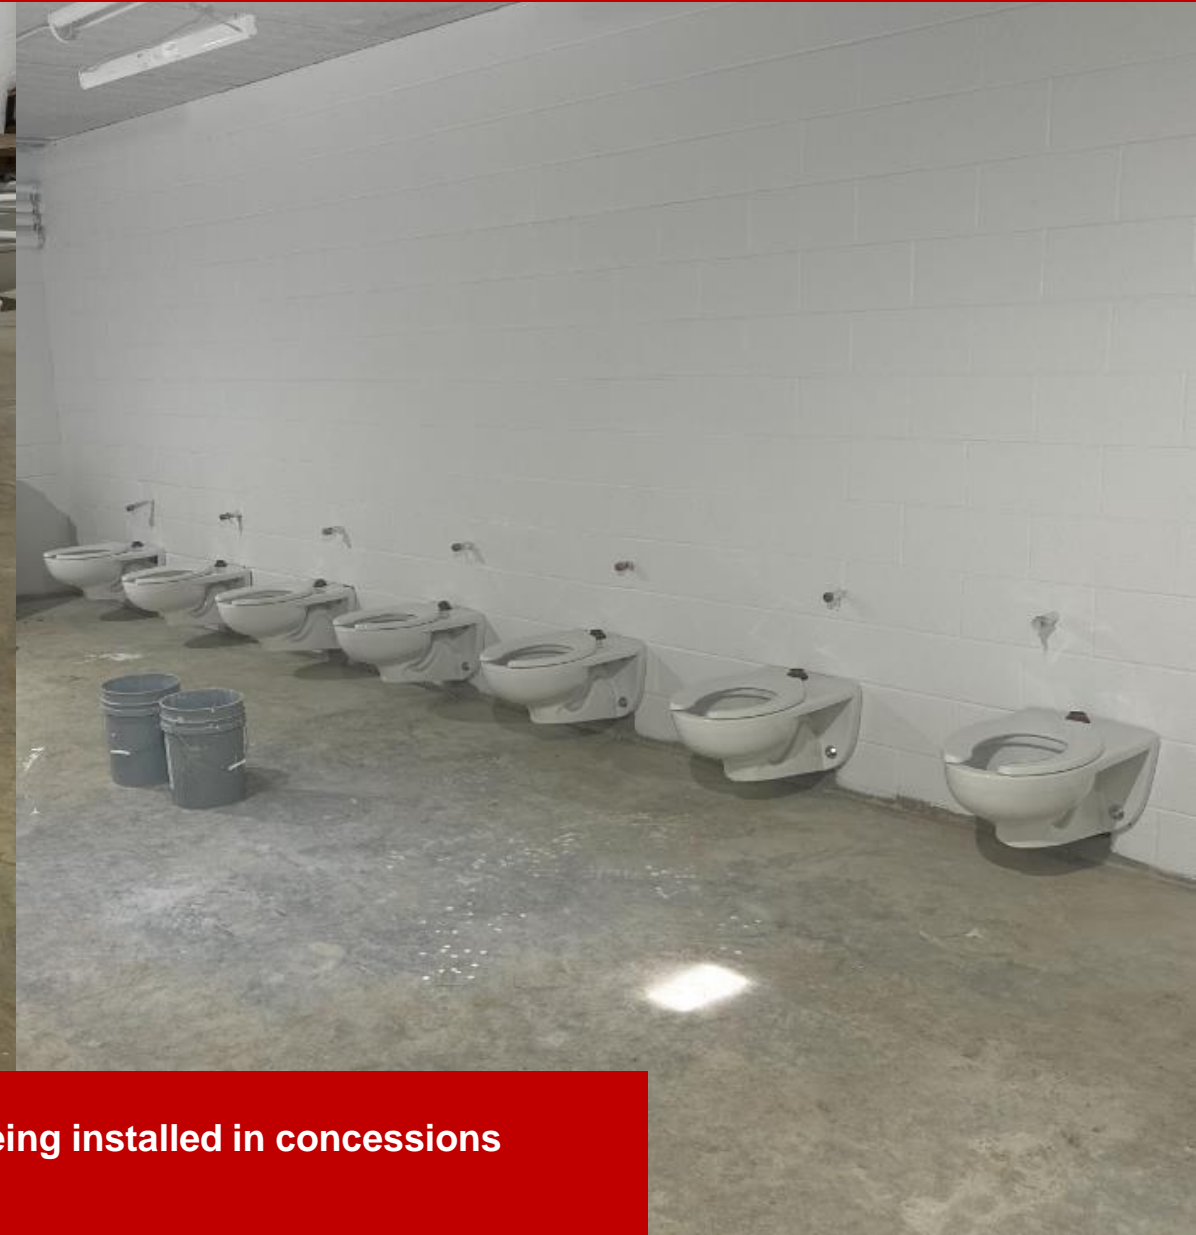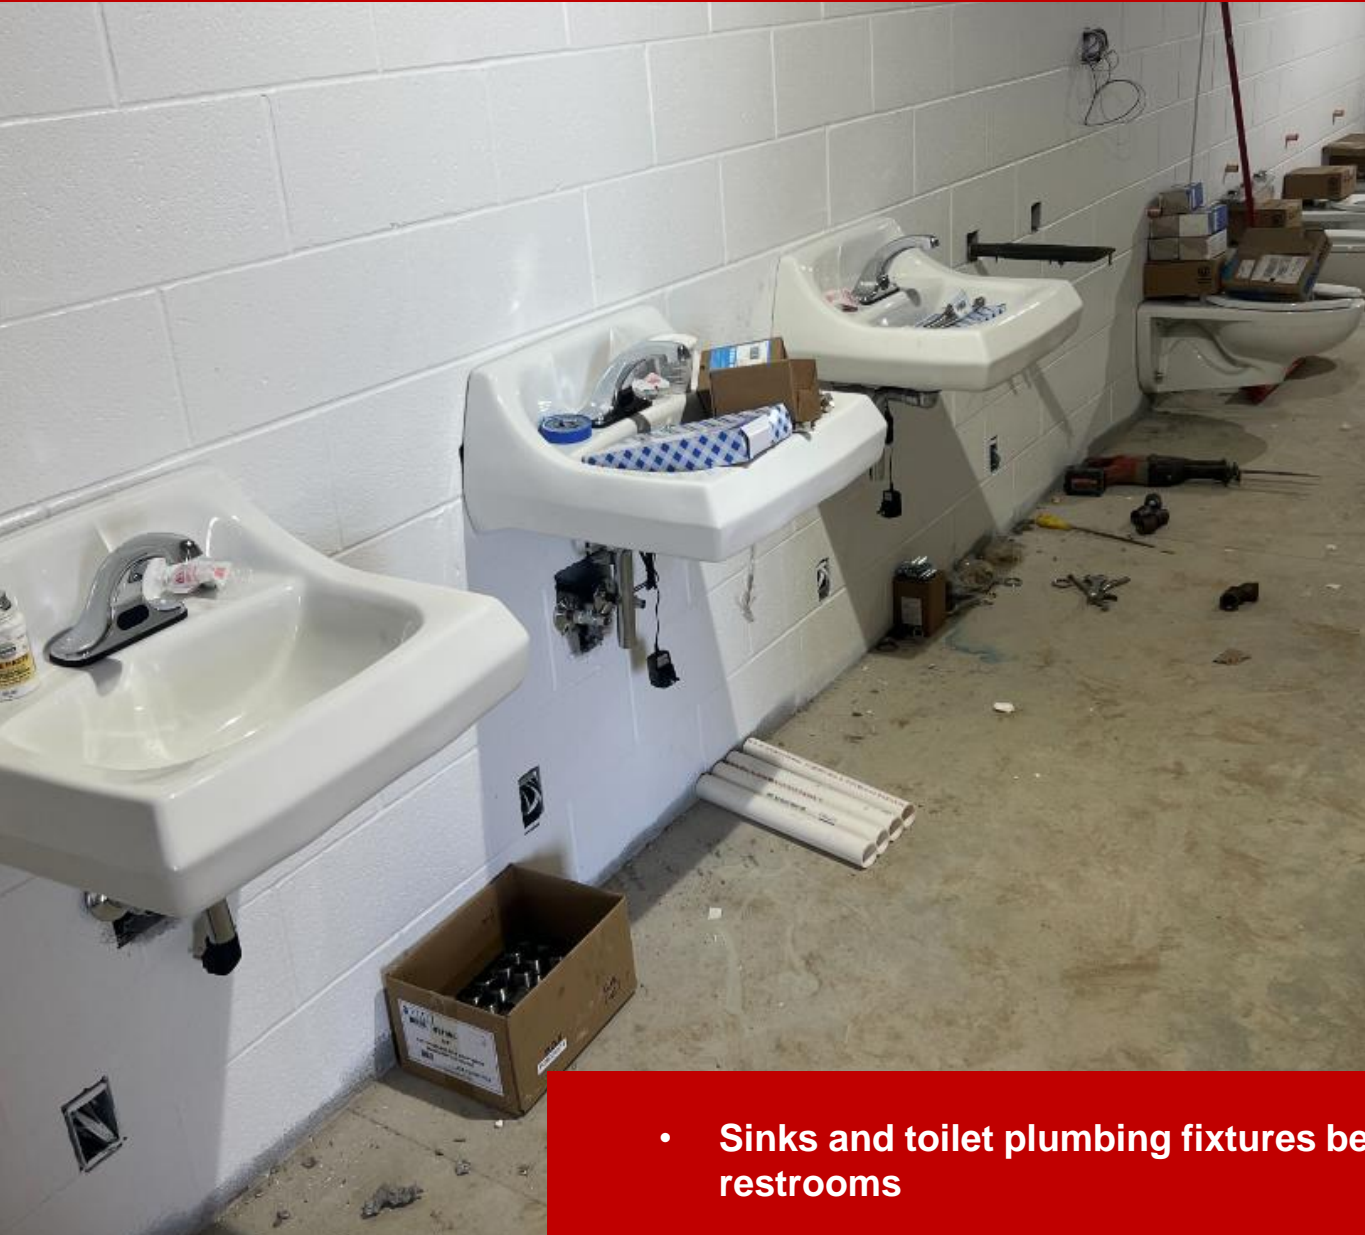

- Sinks and toilet plumbing fixtures being installed in concessions restrooms



# STADIUM SITE WORK OVERVIEW



- Forming and pouring frost wall concrete stoops around exterior doors and entrances before pouring sidewalks.



# STADIUM SITE WORK OVERVIEW



- Rerouting watermain around concessions building so pipe is not located under concessions building



# STADIUM SITE WORK OVERVIEW



- Prepping and pouring concrete for site lighting poles.



# PRIMARY SITE WORK OVERVIEW



- Exterior masonry 100% complete



# PRIMARY SITE WORK OVERVIEW



- Asphalt milling complete and resurfacing scheduled for July 27<sup>th</sup> & 28<sup>th</sup>.



# PRIMARY SITE WORK OVERVIEW





# TWO WEEK LOOK AHEAD



## **Primary Building**

- ▶ Start aluminum framing & glazing.
- ▶ Install casework & countertops at classrooms.
- ▶ Begin ceiling grid & locker install.

## **Stadium & Entrance Buildings**

- ▶ Begin metal panel install at concession building.
- ▶ Pour sidewalk around south end of track.
- ▶ Complete power and data install at press box.
- ▶ Finish grade green belt areas for seeding.
- ▶ Apply resinous flooring & set stainless steel countertops.
