





Activity Summary Report

1. Construction Progress
 - a. Last 30-Days Activities:
 - i. Over excavation and re-compaction for high school classroom wing is complete
 - ii. Cut opening and install exterior door at SW side of existing gym is complete
 - iii. Pour foundation footings and grade beams is ongoing
 - b. Next 30 Days Activities
 - i. Prep and pour remainder of foundation for HS classroom wing and commons
 - ii. Underground plumbing
 - iii. Underground electrical
 - iv. Foundation damp proofing and insulation
 - v. Foundation backfill and compaction
 - vi. Load bearing masonry
2. Furniture, Fixtures & Equipment
 - a. A meeting was held on January 11th to review the preliminary furniture layouts. Meteor will update layouts using district feedback and reissue for review prior to the next meeting scheduled for January 27th.
3. Site Photos / Survey
 - a. On the following pages, please see the progress photos.

- continued -



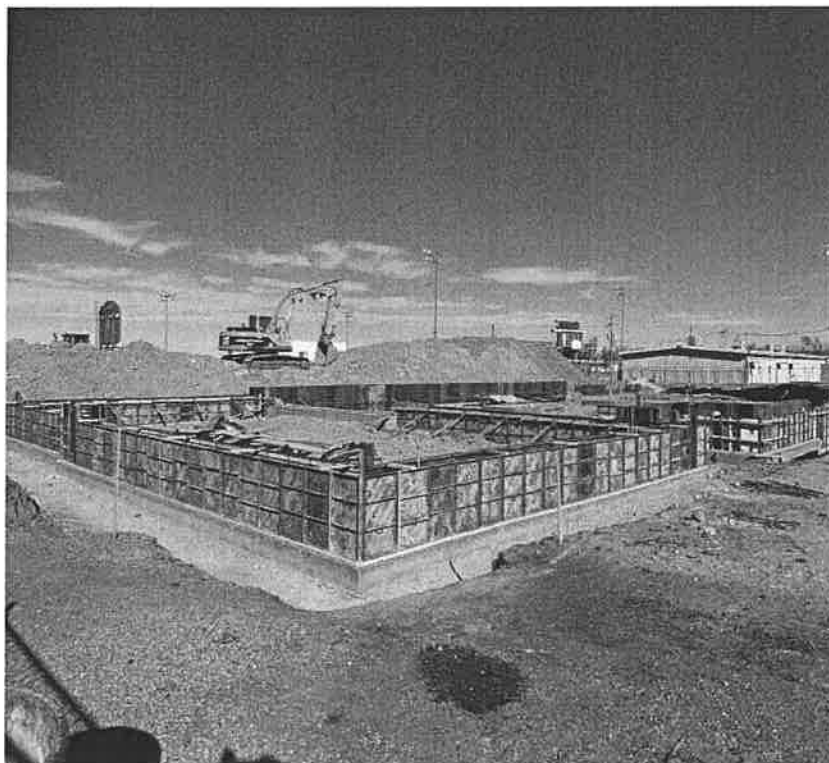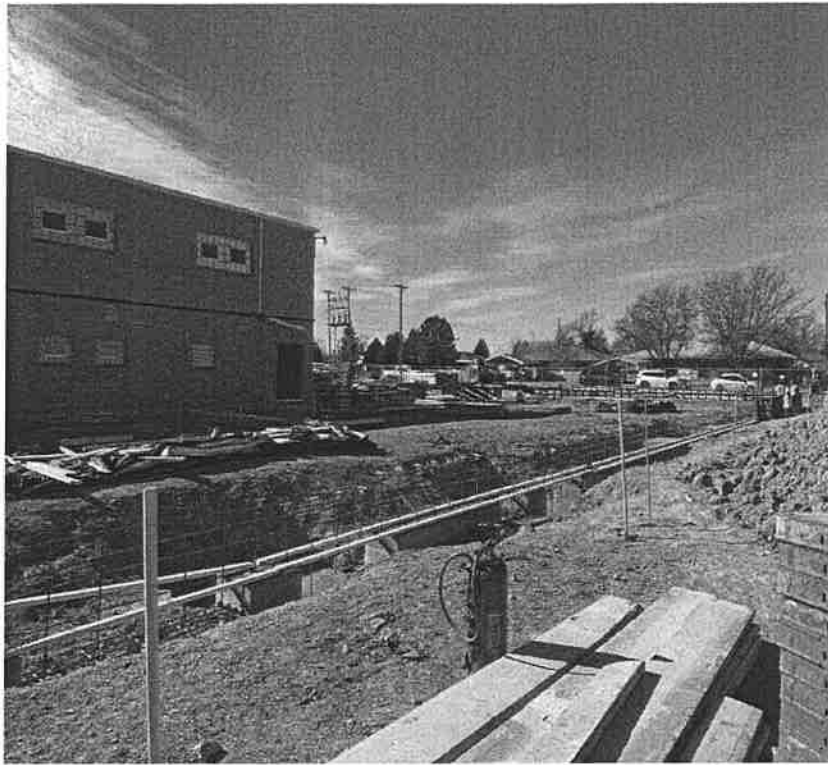



- End of Document -
