



# HURON VALLEY SCHOOLS 2020 Bond Program

## Bid Pack #5 - Construction Progress Update

5/2/22

### Apollo Early Childhood Center



Steel Framing, Cold Formed Metal Stud Framing,  
Densglass Sheathing and CMU are complete



Plumbing drainage piping for canopy roof sump and  
electrical rough-in for canopy soffit lighting is installed



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Apollo Early Childhood Center**



Electrical service to Apollo monument sign is installed



Sand prep and underslab electrical and plumbing are installed and ready for floor slab pour.






**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Apollo Early Childhood Center**



Sand prep and underslab electrical and plumbing are installed and ready for floor slab pour.

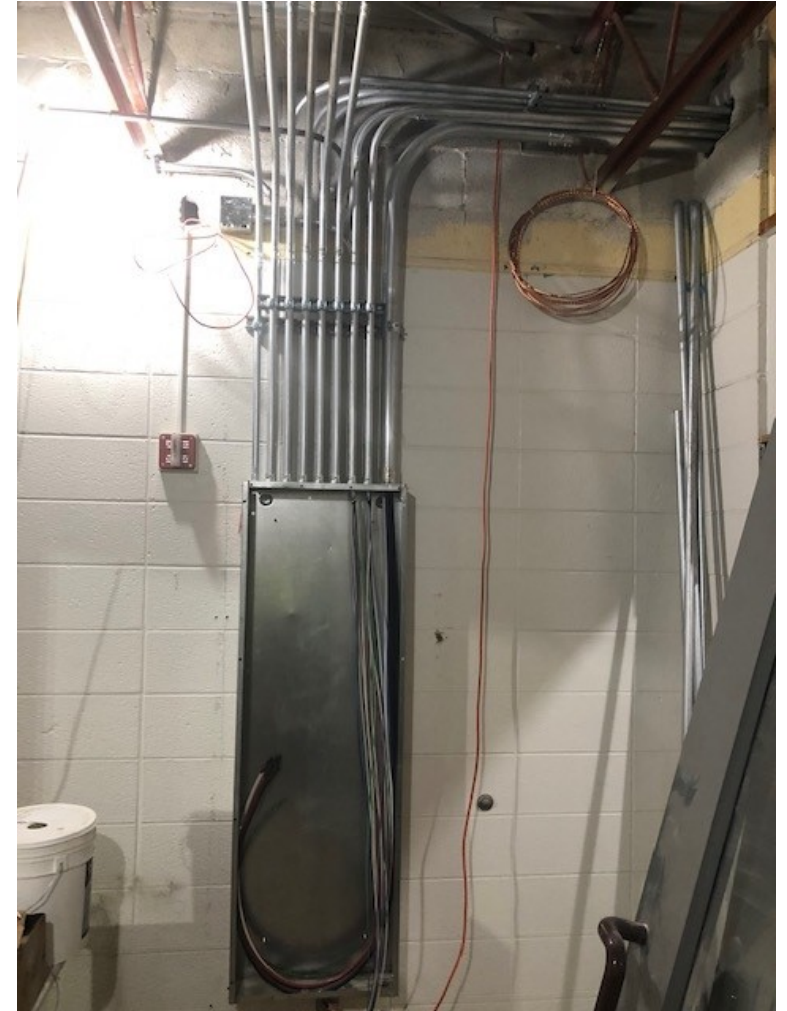

Tub for new Power Distribution Panel RP-L is installed in Storage Room near school office area.



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Country Oaks Elementary School**



Structural Steel Framing is 75% complete; exterior masonry walls are underway; damp proofing is being applied at base of masonry walls



Structural Steel Framing is 75% complete; exterior masonry walls are underway; damp proofing is being applied at base of masonry walls





**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Country Oaks Elementary School**



Stone has been placed around the perimeter of the addition to provide a stable base for trades to work safely



Steel framing for the entrance canopy is remaining to be erected





# HURON VALLEY SCHOOLS 2020 Bond Program

## Bid Pack #5 - Construction Progress Update

5/2/22

### Heritage Elementary School



Structural Steel Framing is 90% complete; exterior masonry walls are built; damp proofing has been applied at base of masonry walls and face brick has started



Ironworkers are completing detailing of entrance canopy steel and tube steel lintels





# HURON VALLEY SCHOOLS 2020 Bond Program

## Bid Pack #5 - Construction Progress Update

5/2/22

### Heritage Elementary School



Ironworkers are completing detailing of entrance canopy steel and tube steel lintels



Structural Steel Framing is 90% complete; exterior masonry walls are built; damp proofing has been applied at base of masonry walls and face brick has started



# HURON VALLEY SCHOOLS 2020 Bond Program

Bid Pack #5 - Construction Progress Update

5/2/22

## Heritage Elementary School



Interior of secured entrance addition is graded off and ready for sand fill material to prepare for slab on grade





**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Kurtz Elementary School**



Erection of structural steel framing for Secured Entry Addition is complete and ready for exterior cold formed metal framing to start



View of new entrance corridor adjacent to Reception and new Main Office area





# HURON VALLEY SCHOOLS 2020 Bond Program

Bid Pack #5 - Construction Progress Update

5/2/22

## Kurtz Elementary School



Exterior masonry walls and damp proofing are in place. Due to extensive rains causing the ground to become soft and muddy, stone has been spread around the perimeter of addition to provide a stable surface for trades to work safely



Interior underground plumbing for new Clinic Toilet room in the School Main Office area





**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Kurtz Elementary School**



Exterior masonry walls and damp proofing are in place. Due to extensive rains causing the ground to become soft and muddy, stone has been spread around the perimeter of addition to provide a stable surface for trades to work safely



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Spring Mills Elementary School**



North wall of the new gymnasium is 50% complete



North wall of the new gymnasium is 50% complete





**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Spring Mills Elementary School**



East wall of the new gymnasium is 50% complete



Interior masonry walls for new Art Classroom are  
being built



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/2/22

**Spring Mills Elementary School**



Existing Chiller is being left in place and is in operation until school is out in June



CMU at the east wall of the new Classroom and Art Classroom is topped off
