


ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
1	↓	SEBRSD Performance Contract	280 days	Wed 5/1/19	Wed 5/27/20	[Gantt bar from Jan to Apr]			
2	↓	Contract Award	1 wk	Wed 5/1/19	Tue 5/7/19	[Task bar]			
3	↓	Kickoff Meeting	1 day	Wed 5/8/19	Wed 5/8/19	[Task bar]			
4	↓	End of Heating Season	0 days	Wed 5/15/19	Wed 5/15/19	[Task bar]			
5	↓	Last Day of School	0 days	Tue 6/18/19	Tue 6/18/19	[Task bar]			
6	↓	First Day of School	0 days	Wed 8/28/19	Wed 8/28/19	[Task bar]			
7	↓	Beginning of Heating Season	0 days	Tue 10/15/19	Tue 10/15/19	[Task bar]			
8	↓	FIM-1 Lighting Upgrades	165 days	Wed 5/8/19	Tue 12/24/19	[Gantt bar from May to Dec]			
9	↓	Submittal Preparation	4 wks	Wed 5/8/19	Tue 6/4/19	[Task bar]			
10	↓	Submittal Review	2 wks	Wed 6/5/19	Tue 6/18/19	[Task bar]			
11	↓	Order Material	6 wks	Wed 6/19/19	Tue 7/30/19	[Task bar]			
12	↓	David Prouty High School	55 days	Wed 7/31/19	Tue 10/15/19	[Gantt bar from July to Oct]			
13	↓	Installation	6 wks	Wed 7/31/19	Tue 9/10/19	[Task bar]			
14	↓	Commissioning	2 wks	Wed 9/11/19	Tue 9/24/19	[Task bar]			
15	↓	Substantial Completion	0 days	Wed 9/25/19	Wed 9/25/19	[Task bar]			
16	↓	Punch List	2 wks	Wed 9/25/19	Tue 10/8/19	[Task bar]			
17	↓	Training	1 wk	Wed 10/9/19	Tue 10/15/19	[Task bar]			
18	↓	Knox Trail Middle School	65 days	Wed 7/31/19	Tue 10/29/19	[Gantt bar from July to Oct]			
19	↓	Installation	8 wks	Wed 7/31/19	Tue 9/24/19	[Task bar]			
20	↓	Commissioning	2 wks	Wed 9/25/19	Tue 10/8/19	[Task bar]			
21	↓	Substantial Completion	0 days	Wed 10/9/19	Wed 10/9/19	[Task bar]			
22	↓	Punch List	2 wks	Wed 10/9/19	Tue 10/22/19	[Task bar]			
23	↓	Training	1 wk	Wed 10/23/19	Tue 10/29/19	[Task bar]			
24	↓	Wire Village Elementary School	65 days	Wed 9/25/19	Tue 12/24/19	[Gantt bar from Sept to Dec]			
25	↓	Installation	8 wks	Wed 9/25/19	Tue 11/19/19	[Task bar]			
26	↓	Commissioning	2 wks	Wed 11/20/19	Tue 12/3/19	[Task bar]			
27	↓	Substantial Completion	0 days	Wed 12/4/19	Wed 12/4/19	[Task bar]			
28	↓	Punch List	2 wks	Wed 12/4/19	Tue 12/17/19	[Task bar]			


Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
29		Training	1 wk	Wed 12/18/19	Tue 12/24/19				
30		East Brookfield Elementary School	65 days	Wed 9/18/19	Tue 12/17/19				
31		Installation	8 wks	Wed 9/18/19	Tue 11/12/19				
32		Commissioning	2 wks	Wed 11/13/19	Tue 11/26/19				
33		Substantial Completion	0 days	Wed 11/27/19	Wed 11/27/19				
34		Punch List	2 wks	Wed 11/27/19	Tue 12/10/19				
35		Training	1 wk	Wed 12/11/19	Tue 12/17/19				
36		School Administration Building	7 days	Wed 9/11/19	Thu 9/19/19				
37		Installation	1 wk	Wed 9/11/19	Tue 9/17/19				
38		Commissioning	1 day	Wed 9/18/19	Wed 9/18/19				
39		Substantial Completion	0 days	Thu 9/19/19	Thu 9/19/19				
40		Punch List	1 day	Thu 9/19/19	Thu 9/19/19				
41		FIM-2 Plug Loads	73 days	Wed 5/8/19	Fri 8/16/19				
42		Submittal Preparation	2 wks	Wed 5/8/19	Tue 5/21/19				
43		Submittal Review	1 wk	Wed 5/22/19	Tue 5/28/19				
44		Order Material	2 wks	Wed 5/29/19	Tue 6/11/19				
45		David Prouty High School	16 days	Wed 6/12/19	Wed 7/3/19				
46		Installation	2 wks	Wed 6/12/19	Tue 6/25/19				
47		Commissioning	1 wk	Wed 6/26/19	Tue 7/2/19				
48		Substantial Completion	0 days	Wed 7/3/19	Wed 7/3/19				
49		Punch List	1 day	Wed 7/3/19	Wed 7/3/19				
50		Knox Trail Middle School	16 days	Wed 6/26/19	Wed 7/17/19				
51		Installation	2 wks	Wed 6/26/19	Tue 7/9/19				
52		Commissioning	1 wk	Wed 7/10/19	Tue 7/16/19				
53		Substantial Completion	0 days	Wed 7/17/19	Wed 7/17/19				
54		Punch List	1 day	Wed 7/17/19	Wed 7/17/19				
55		Wire Village Elementary School	16 days	Wed 7/10/19	Wed 7/31/19				
56		Installation	2 wks	Wed 7/10/19	Tue 7/23/19				

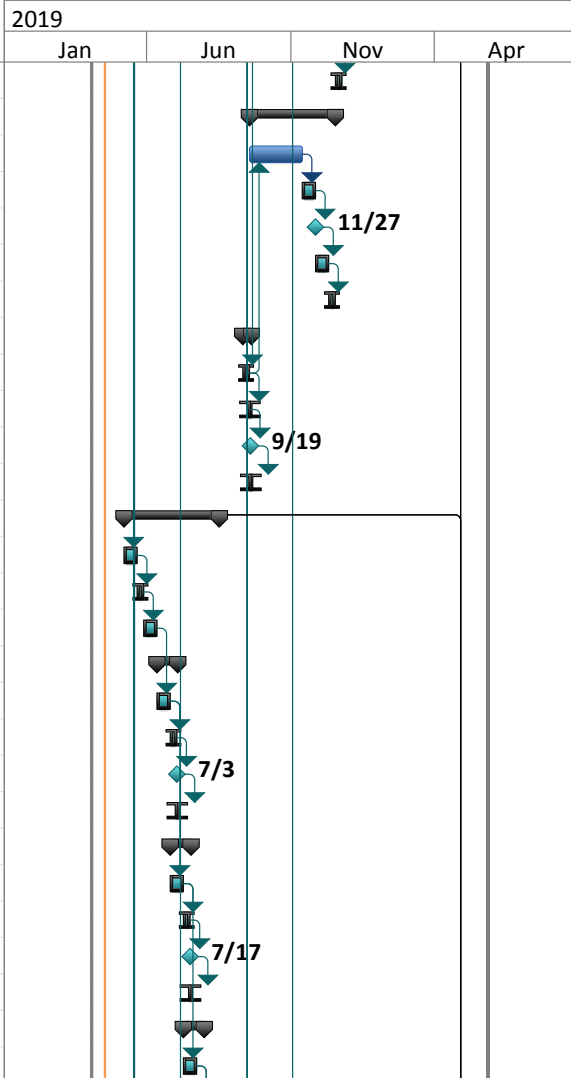

Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
57		Commissioning	1 wk	Wed 7/24/19	Tue 7/30/19				
58		Substantial Completion	0 days	Wed 7/31/19	Wed 7/31/19				
59		Punch List	1 day	Wed 7/31/19	Wed 7/31/19				
60		East Brookfield Elementary School	16 days	Wed 7/24/19	Wed 8/14/19				
61		Installation	2 wks	Wed 7/24/19	Tue 8/6/19				
62		Commissioning	1 wk	Wed 8/7/19	Tue 8/13/19				
63		Substantial Completion	0 days	Wed 8/14/19	Wed 8/14/19				
64		Punch List	1 day	Wed 8/14/19	Wed 8/14/19				
65		School Administration Building	8 days	Wed 8/7/19	Fri 8/16/19				
66		Installation	1 wk	Wed 8/7/19	Tue 8/13/19				
67		Commissioning	2 days	Wed 8/14/19	Thu 8/15/19				
68		Substantial Completion	0 days	Fri 8/16/19	Fri 8/16/19				
69		Punch List	1 day	Fri 8/16/19	Fri 8/16/19				
70		FIM-3 Building Envelope	110 days	Wed 5/8/19	Tue 10/8/19				
71		Submittal Preparation	2 wks	Wed 5/8/19	Tue 5/21/19				
72		Submittal Review	1 wk	Wed 5/22/19	Tue 5/28/19				
73		Order Material	2 wks	Wed 5/29/19	Tue 6/11/19				
74		David Prouty High School	30 days	Tue 6/18/19	Mon 7/29/19				
75		Installation	4 wks	Tue 6/18/19	Mon 7/15/19				
76		Commissioning	1 wk	Tue 7/16/19	Mon 7/22/19				
77		Substantial Completion	0 days	Tue 7/23/19	Tue 7/23/19				
78		Punch List	1 wk	Tue 7/23/19	Mon 7/29/19				
79		Knox Trail Middle School	30 days	Tue 7/16/19	Mon 8/26/19				
80		Installation	4 wks	Tue 7/16/19	Mon 8/12/19				
81		Commissioning	1 wk	Tue 8/13/19	Mon 8/19/19				
82		Substantial Completion	0 days	Tue 8/20/19	Tue 8/20/19				
83		Punch List	1 wk	Tue 8/20/19	Mon 8/26/19				
84		Wire Village Elementary School	25 days	Tue 8/13/19	Mon 9/16/19				

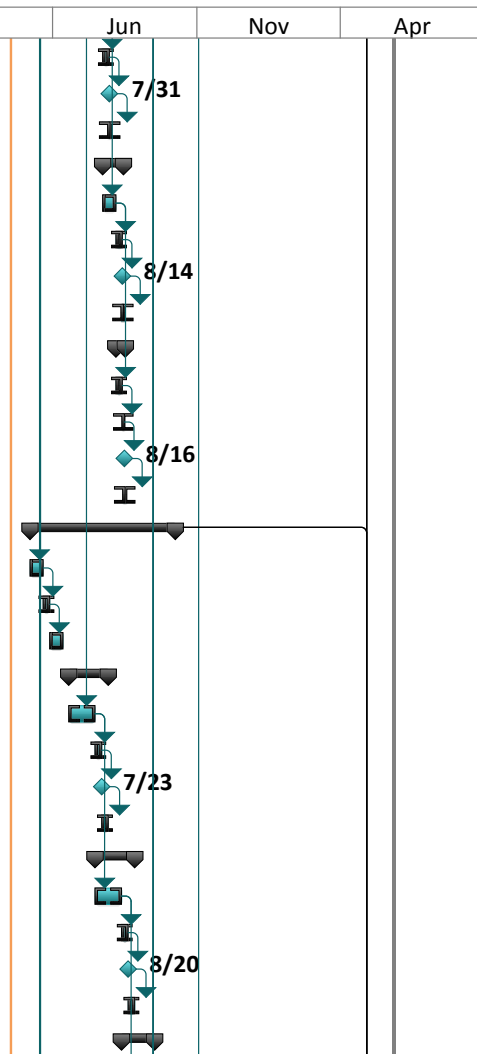


Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
85		Installation	3 wks	Tue 8/13/19	Mon 9/2/19				
86		Commissioning	1 wk	Tue 9/3/19	Mon 9/9/19				
87		Substantial Completion	0 days	Tue 9/10/19	Tue 9/10/19				
88		Punch List	1 wk	Tue 9/10/19	Mon 9/16/19				
89		East Brookfield Elementary School	25 days	Tue 9/3/19	Mon 10/7/19				
90		Installation	3 wks	Tue 9/3/19	Mon 9/23/19				
91		Commissioning	1 wk	Tue 9/24/19	Mon 9/30/19				
92		Substantial Completion	0 days	Tue 10/1/19	Tue 10/1/19				
93		Punch List	1 wk	Tue 10/1/19	Mon 10/7/19				
94		School Administration Building	11 days	Tue 9/24/19	Tue 10/8/19				
95		Installation	1 wk	Tue 9/24/19	Mon 9/30/19				
96		Commissioning	1 wk	Tue 10/1/19	Mon 10/7/19				
97		Substantial Completion	0 days	Tue 10/8/19	Tue 10/8/19				
98		Punch List	1 day	Tue 10/8/19	Tue 10/8/19				
99		FIM-5 Energy Management System	255 days	Wed 5/8/19	Tue 4/28/20				
100		Submittal Preparation	8 wks	Wed 5/8/19	Tue 7/2/19				
101		Submittal Review	5 days	Wed 7/3/19	Tue 7/9/19				
102		Order Material	4 wks	Wed 7/10/19	Tue 8/6/19				
103		David Prouty High School	133 days	Wed 8/7/19	Fri 2/7/20				
104		Installation	8 wks	Wed 8/7/19	Tue 10/1/19				
105		Commissioning	12 wks	Wed 10/2/19	Tue 12/24/19				
106		Substantial Completion	0 days	Wed 12/25/19	Wed 12/25/19				
107		Punch List	6 wks	Wed 12/25/19	Tue 2/4/20				
108		Training	3 days	Wed 2/5/20	Fri 2/7/20				
109		Knox Trail Middle School	190 days	Wed 8/7/19	Tue 4/28/20				
110		Installation	25 wks	Wed 8/7/19	Tue 1/28/20				
111		Commissioning	8 wks	Wed 1/29/20	Tue 3/24/20				
112		Substantial Completion	0 days	Wed 3/25/20	Wed 3/25/20				


Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
113		Punch List	4 wks	Wed 3/25/20	Tue 4/21/20				
114		Training	1 wk	Wed 4/22/20	Tue 4/28/20				
115		Wire Village Elementary School	55 days	Wed 10/2/19	Tue 12/17/19				
116		Installation	4 wks	Wed 10/2/19	Tue 10/29/19				
117		Commissioning	4 wks	Wed 10/30/19	Tue 11/26/19				
118		Substantial Completion	0 days	Wed 11/27/19	Wed 11/27/19				
119		Punch List	2 wks	Wed 11/27/19	Tue 12/10/19				
120		Training	1 wk	Wed 12/11/19	Tue 12/17/19				
121		East Brookfield Elementary School	105 days	Wed 10/2/19	Tue 2/25/20				
122		Installation	12 wks	Wed 10/2/19	Tue 12/24/19				
123		Commissioning	4 wks	Wed 12/25/19	Tue 1/21/20				
124		Substantial Completion	0 days	Wed 1/22/20	Wed 1/22/20				
125		Punch List	4 wks	Wed 1/22/20	Tue 2/18/20				
126		Training	5 days	Wed 2/19/20	Tue 2/25/20				
127		School Administration Building	55 days	Wed 8/7/19	Wed 10/23/19				
128		Installation	2 wks	Wed 8/7/19	Tue 8/20/19				
129		Commissioning	1 wk	Tue 10/15/19	Mon 10/21/19				
130		Substantial Completion	0 days	Tue 10/22/19	Tue 10/22/19				
131		Punch List	1 day	Tue 10/22/19	Tue 10/22/19				
132		Training	0 days	Wed 10/23/19	Wed 10/23/19				
133		FIM-6 Kitchen Hood Controls	97 days	Wed 5/8/19	Thu 9/19/19				
134		Submittal Preparation	1 wk	Wed 5/8/19	Tue 5/14/19				
135		Submittal Review	1 wk	Wed 5/15/19	Tue 5/21/19				
136		Order Material	4 wks	Wed 5/22/19	Tue 6/18/19				
137		David Prouty High School	66 days	Wed 6/19/19	Wed 9/18/19				
138		Installation	1 wk	Wed 6/19/19	Tue 6/25/19				
139		Commissioning	1 wk	Wed 9/4/19	Tue 9/10/19				
140		Substantial Completion	1 day	Wed 9/11/19	Wed 9/11/19				

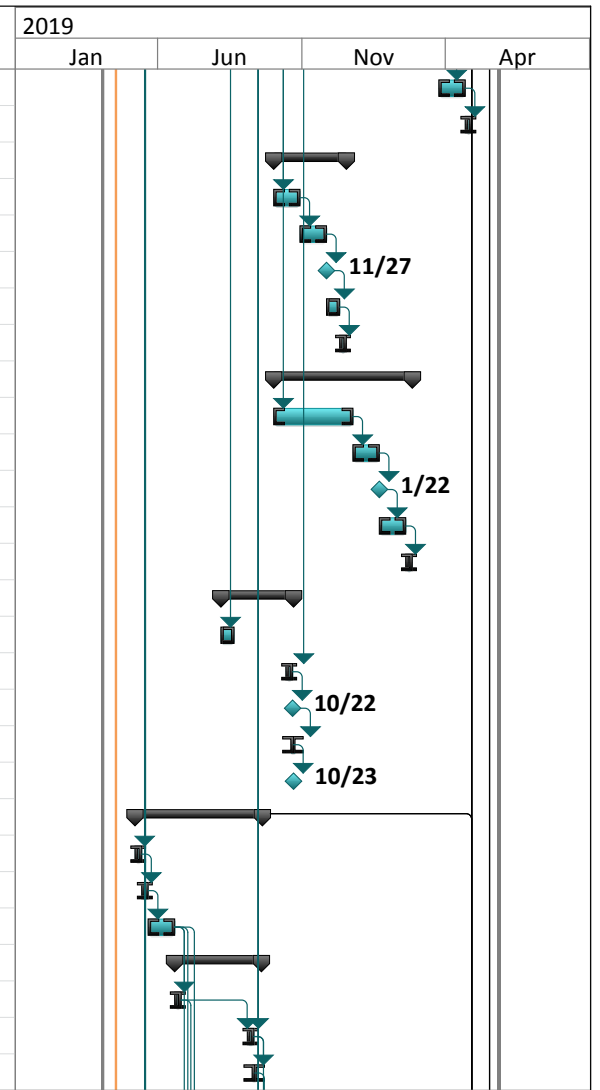

Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
141		Punch List	1 wk	Thu 9/12/19	Wed 9/18/19				
142		Training	0 days	Wed 9/11/19	Wed 9/11/19				
143		Knox Trail Middle School	61 days	Wed 6/26/19	Wed 9/18/19				
144		Installation	1 wk	Wed 6/26/19	Tue 7/2/19				
145		Commissioning	1 wk	Wed 9/4/19	Tue 9/10/19				
146		Substantial Completion	1 day	Wed 9/11/19	Wed 9/11/19				
147		Punch List	1 wk	Thu 9/12/19	Wed 9/18/19				
148		Training	0 days	Wed 9/11/19	Wed 9/11/19				
149		Wire Village Elementary School	56 days	Wed 7/3/19	Wed 9/18/19				
150		Installation	1 wk	Wed 7/3/19	Tue 7/9/19				
151		Commissioning	1 wk	Wed 9/4/19	Tue 9/10/19				
152		Substantial Completion	1 day	Wed 9/11/19	Wed 9/11/19				
153		Punch List	1 wk	Thu 9/12/19	Wed 9/18/19				
154		Training	0 days	Wed 9/11/19	Wed 9/11/19				
155		East Brookfield Elementary School	52 days	Wed 7/10/19	Thu 9/19/19				
156		Installation	1 wk	Wed 7/10/19	Tue 7/16/19				
157		Commissioning	1 wk	Wed 9/4/19	Tue 9/10/19				
158		Substantial Completion	1 day	Thu 9/12/19	Thu 9/12/19				
159		Punch List	1 wk	Fri 9/13/19	Thu 9/19/19				
160		Training	0 days	Wed 9/11/19	Wed 9/11/19				
161		FIM-7 Walk-In Cooler Controls	86 days	Thu 5/9/19	Thu 9/5/19				
162		Submittal Preparation	1 wk	Thu 5/9/19	Wed 5/15/19				
163		Submittal Review	1 wk	Thu 5/16/19	Wed 5/22/19				
164		Order Material	4 wks	Thu 5/23/19	Wed 6/19/19				
165		David Prouty High School	55 days	Thu 6/20/19	Wed 9/4/19				
166		Installation	1 wk	Thu 6/20/19	Wed 6/26/19				
167		Commissioning	1 wk	Thu 6/27/19	Wed 7/3/19				
168		Substantial Completion	1 day	Thu 7/4/19	Thu 7/4/19				

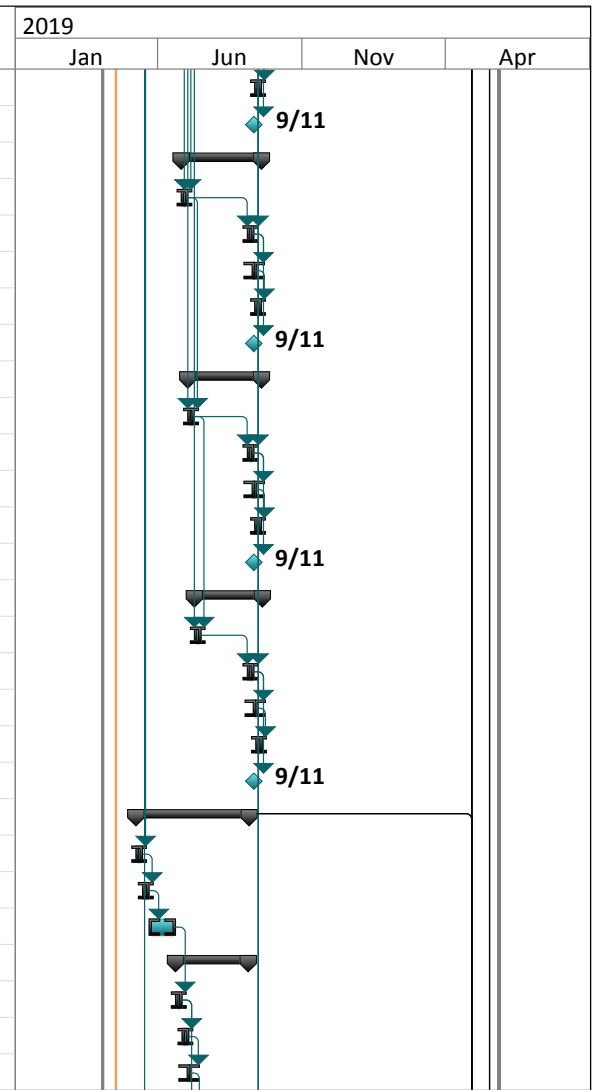

Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
169		Punch List	1 wk	Fri 7/5/19	Thu 7/11/19				
170		Training	1 day	Wed 9/4/19	Wed 9/4/19				
171		Knox Trail Middle School	50 days	Thu 6/27/19	Wed 9/4/19				
172		Installation	1 wk	Thu 6/27/19	Wed 7/3/19				
173		Commissioning	1 wk	Thu 7/4/19	Wed 7/10/19				
174		Substantial Completion	1 day	Thu 7/11/19	Thu 7/11/19				
175		Punch List	1 wk	Fri 7/12/19	Thu 7/18/19				
176		Training	1 day	Wed 9/4/19	Wed 9/4/19				
177		Wire Village Elementary School	46 days	Thu 7/4/19	Thu 9/5/19				
178		Installation	1 wk	Thu 7/4/19	Wed 7/10/19				
179		Commissioning	1 wk	Thu 7/11/19	Wed 7/17/19				
180		Substantial Completion	1 day	Thu 7/18/19	Thu 7/18/19				
181		Punch List	1 wk	Fri 7/19/19	Thu 7/25/19				
182		Training	1 day	Thu 9/5/19	Thu 9/5/19				
183		East Brookfield Elementary School	41 days	Thu 7/11/19	Thu 9/5/19				
184		Installation	1 wk	Thu 7/11/19	Wed 7/17/19				
185		Commissioning	1 wk	Thu 7/18/19	Wed 7/24/19				
186		Substantial Completion	1 day	Thu 7/25/19	Thu 7/25/19				
187		Punch List	1 wk	Fri 7/26/19	Thu 8/1/19				
188		Training	1 day	Thu 9/5/19	Thu 9/5/19				
189		FIM-9 Boiler Replacements	193 days	Wed 5/8/19	Fri 1/31/20				
190		Submittal Preparation	8 days	Wed 5/8/19	Fri 5/17/19				
191		Submittal Review	1 wk	Mon 5/20/19	Fri 5/24/19				
192		Order Material	6 wks	Mon 5/27/19	Fri 7/5/19				
193		Knox Trail Middle School	150 days	Mon 7/8/19	Fri 1/31/20				
194		Installation	12 wks	Mon 7/8/19	Fri 9/27/19				
195		Start-up	2 wks	Mon 9/30/19	Fri 10/11/19				
196		Commissioning	16 wks	Mon 10/14/19	Fri 1/31/20				

Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	2019			
						Jan	Jun	Nov	Apr
197		Substantial Completion	1 wk	Mon 10/14/19	Fri 10/18/19				
198		Punch List	15 wks	Mon 10/21/19	Fri 1/31/20				
199		Training	4 wks	Mon 10/14/19	Fri 11/8/19				
200		Wire Village Elementary School	150 days	Mon 7/8/19	Fri 1/31/20				
201		Installation	12 wks	Mon 7/8/19	Fri 9/27/19				
202		Start-up	2 wks	Mon 9/30/19	Fri 10/11/19				
203		Commissioning	16 wks	Mon 10/14/19	Fri 1/31/20				
204		Substantial Completion	1 wk	Mon 10/14/19	Fri 10/18/19				
205		Punch List	15 wks	Mon 10/21/19	Fri 1/31/20				
206		Training	4 wks	Mon 10/14/19	Fri 11/8/19				
207		East Brookfield Elementary School	150 days	Mon 7/8/19	Fri 1/31/20				
208		Installation	12 wks	Mon 7/8/19	Fri 9/27/19				
209		Start-up	2 wks	Mon 9/30/19	Fri 10/11/19				
210		Commissioning	16 wks	Mon 10/14/19	Fri 1/31/20				
211		Substantial Completion	1 wk	Mon 10/14/19	Fri 10/18/19				
212		Punch List	15 wks	Mon 10/21/19	Fri 1/31/20				
213		Training	4 wks	Mon 10/14/19	Fri 11/8/19				
214		As-Built Preparation	4 wks	Wed 4/29/20	Tue 5/26/20				
215		O&M Manual Preparation	2 wks	Wed 4/29/20	Tue 5/12/20				
216		Closeout Meeting	0 days	Wed 5/27/20	Wed 5/27/20				
217		Final Completion Signoff	0 days	Wed 5/27/20	Wed 5/27/20				
218		Turnover to Measurement & Verification	0 days	Wed 5/27/20	Wed 5/27/20				

Project: SEBRSD Contract Schedul Date: Thu 4/18/19	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
