



Buena Vista School District – New MS / HS Progress Report – June 2020

Project Highlights:

- Architect/Design:
 - TreanorHL (“THL”) has continued visiting the site to document progress and any areas for correction.
 - THL has helped BVSD identify some areas for additional site boulders uncovered during excavation.
 - THL is continuing to respond to submittals and delivered gym floor stain samples to the District early this month.
- Contractor:
 - Haselden and Diesslin (“HD”) completed final grade curb and gutter early this month with pours completing by end of June. Light pole bases also completed this month.
 - HD has been making great progress on the interior as well with drywall and utility installation ongoing.
 - HD poured the MS Gym floor early this month now that the exterior skin has been installed.
- Owner/Procurement:
 - Cooperative Strategies (“CS”) met with the District’s IT consultant to review networking configurations and other technical specifications for the new wing of construction. We have revised specifications for equipment based on their feedback.
 - CS has finalized the orders for smart panels and computers required for Phase B. Coordination between the consultant and HD is ongoing.

- CS met with the District and our keying manufacturer to discuss the key scheme for Phase B. Key orders will be released once hardware is on order and our security plan is confirmed.
- CS continues to finalize quotes for owner furnished items, including the scoring table to be used during basketball games. The new set up will include a table with the BVSD logo and new padded seats with logos.
- CS is continuing to monitor the virus in Colorado and the impact on BVSD. The entire project team is prepared to adapt to any scenario which may develop as we begin to reopen the state.

Upcoming Events:

- Sidewalk installation will soon begin along Railroad Street.
- The MS Gym construction is tracking to complete this month with the HS Gym following behind in sequence.
- MS Locker Room inspections will occur in early July.
- All of us on the construction project wish BV a safe and happy summer, and we hope to see you back in school as soon as possible!


Project Look-Ahead/ Planned Milestones:

Painting Art Rooms	Starting Early July
Restroom Tiles	Completing Early July
Site Paving	July
Roof Completion	Late July
Drywall in Athletic Commons	Mid to Late July


Budget Overview:

Total Project Budget: \$50,862,204.00
Billed to date: \$40,575,111.11
Amount expended: 80%

In June, the Colorado Department of Education processed the nineteenth round of reimbursements from the BEST grant for this project. Current expenditures total about \$40.56 million which is roughly 80% of the total budget of about \$50.8 million.

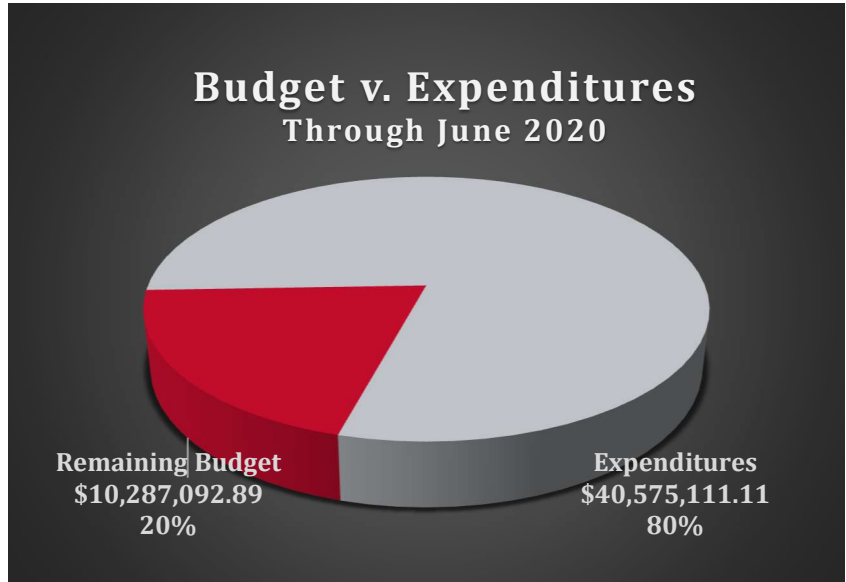

Budget Detail:

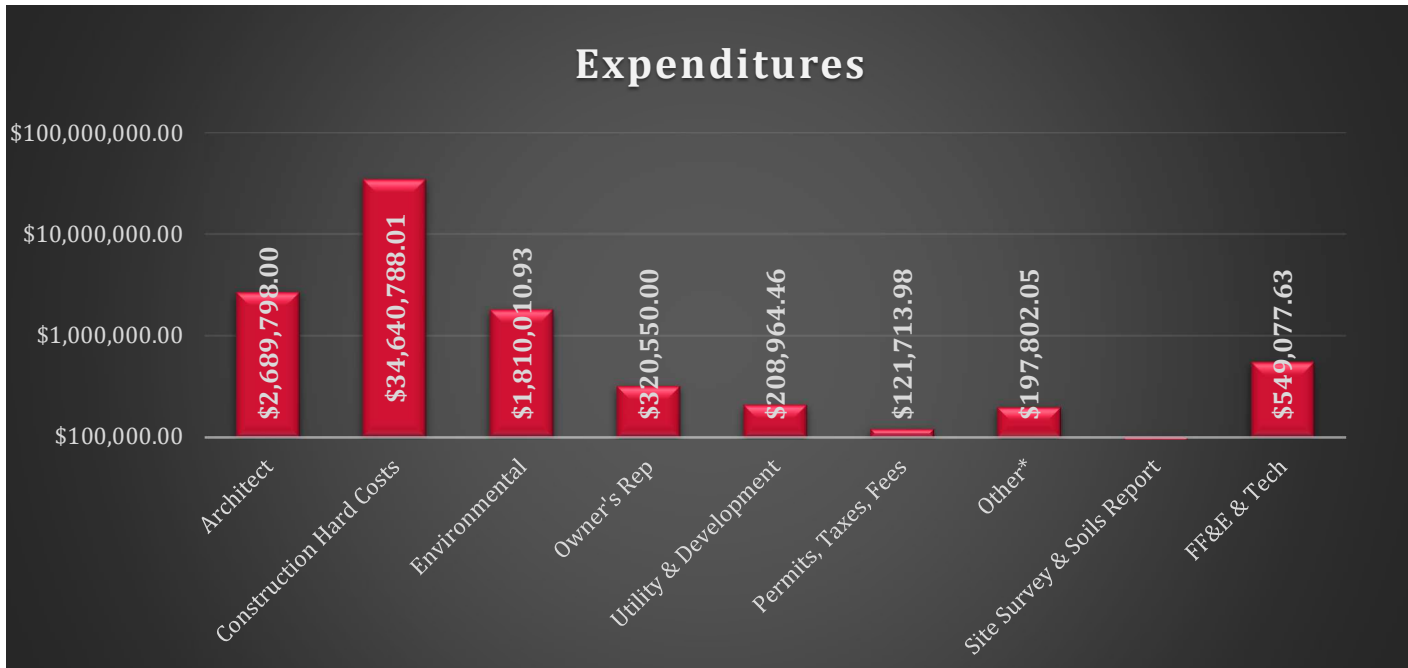

*Other includes fees associated with LEED certification, legal fees, and moving costs

Site Photos – June 2020



The Middle School Gym slab has been poured. (Left)

New tile in the locker rooms is complete (Right)



Window cut outs at the HS Gym Tie-In (Left)
