



Buena Vista School District – New MS / HS Progress Report – August 2020

Project Highlights:

- Architect/Design:
 - TreanorHL (“THL”) visited the site this month to inspect progress and issue their field observation reports. Their direction is critical to ensure the building is constructed as intended.
 - THL produced the BV Victory Bell plaque signage for District approval this month. THL has also been assisting the District with final plans and locations for all parking lot signage.
 - In addition to signage, THL has also been advising the project team on landscaping materials, locker bench locations, and other final details needed before construction completion.
- Contractor:
 - Haselden and Diesslin (“HD”) has continued making progress on the site and inside the building. HD completed the irrigation mains as anticipated and have now moved into branch line irrigation. Sidewalks are also moving ahead as scheduled and are expected to complete early next month.
 - HD preformed the final concrete grind needed before color staining. Final paint will be following the floor polishing throughout the building.
 - HD continues to work closely with the Project Team verifying key details including the installation of sealing expansion joints at the existing gym tie in.
- Owner/Procurement:
 - Cooperative Strategies (“CS”) coordinated delivery of furniture and equipment for the existing gym renovation. New items included training tables for

injury rehab and a therapy tub. The existing gym also received new lockers and locker benches.

- CS is now coordinating the next round of furniture installations for the remaining areas of new construction including lunch tables and art room equipment.
- CS is also coordinating deliveries for all technology equipment in the new phase. Servers and switches will be installed next month, with flat panels and remaining computer equipment to follow.
- CS is closely monitoring other delivery schedules including a new basketball scorers table, the new vending machine, and all the Food Lab appliances.

Upcoming Events:

- Painters will begin applying their final coat starting in the art rooms and moving towards the Athletic Commons.
- The Bell Structure will be placed next month after final locations are verified with BVSD.
- Sidewalks and irrigation tie ins will complete early next month with plantings, topsoil, and other landscaping to follow.


Project Look-Ahead/ Planned Milestones:

Hardwood Court Installation at Gym	Early September
Concrete Floor Staining	Early September
Roof Top Units Online	Mid-September
Kitchen Health Inspections	Early October


Budget Overview:

Total Project Budget: \$50,862,204.00
 Billed to date: \$45,029,034.14
 Amount expended: 89%

In August, the Colorado Department of Education processed the twenty first round of reimbursements from the BEST grant for this project. Current expenditures total about \$45 million which is roughly 89% of the total budget of about \$50.8 million.

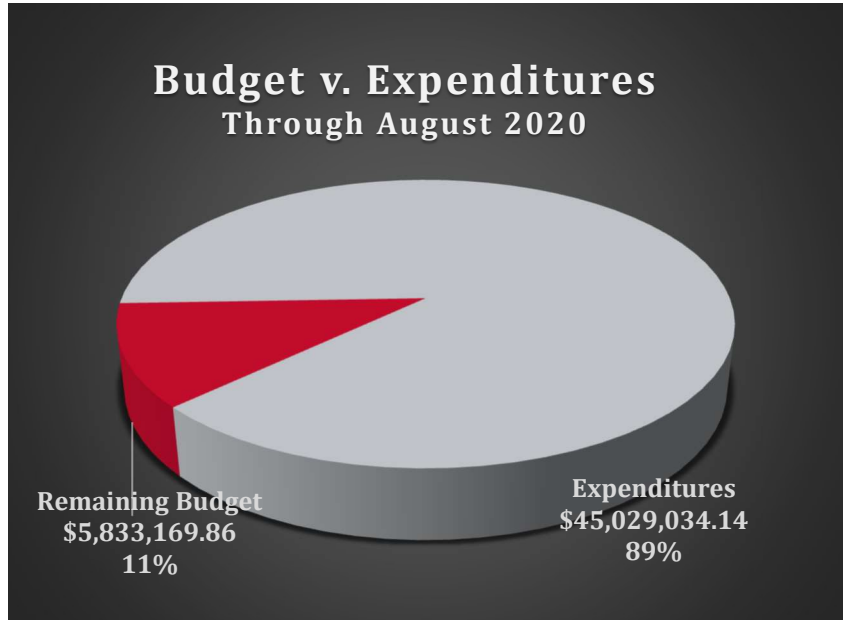

Budget Detail:

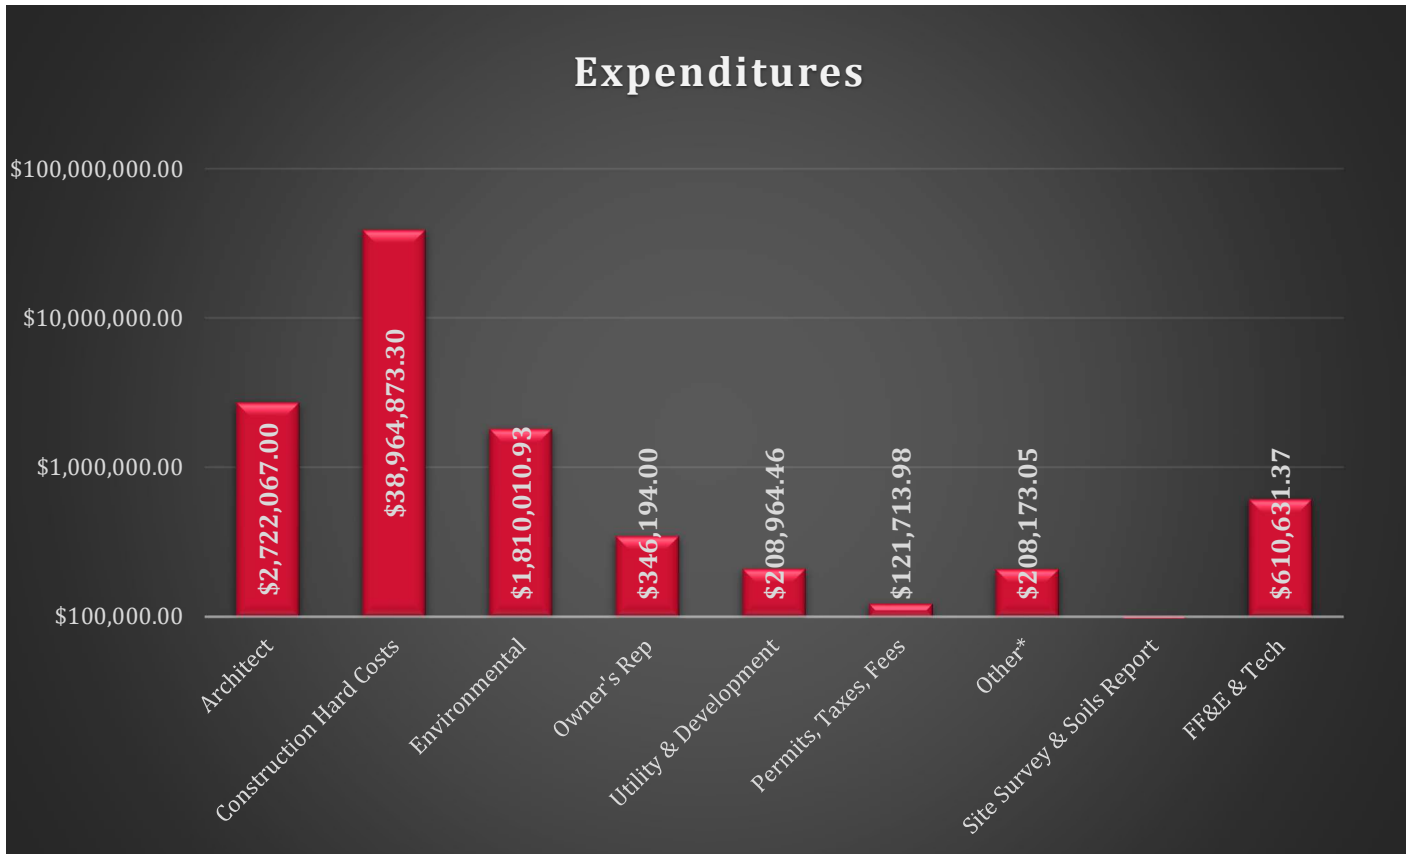

*Other includes fees associated with LEED certification, legal fees, and moving costs

Site Photos – August 2020

Stone work at Athletic
Commons Entrance (right)



Cobble Installation Ongoing

New lockers
and benches
at existing gym.

