


CAPITAL PROJECTS UPDATE MARTIN COUNTY SCHOOL DISTRICT

11/22/2021



Educate All Students for Success

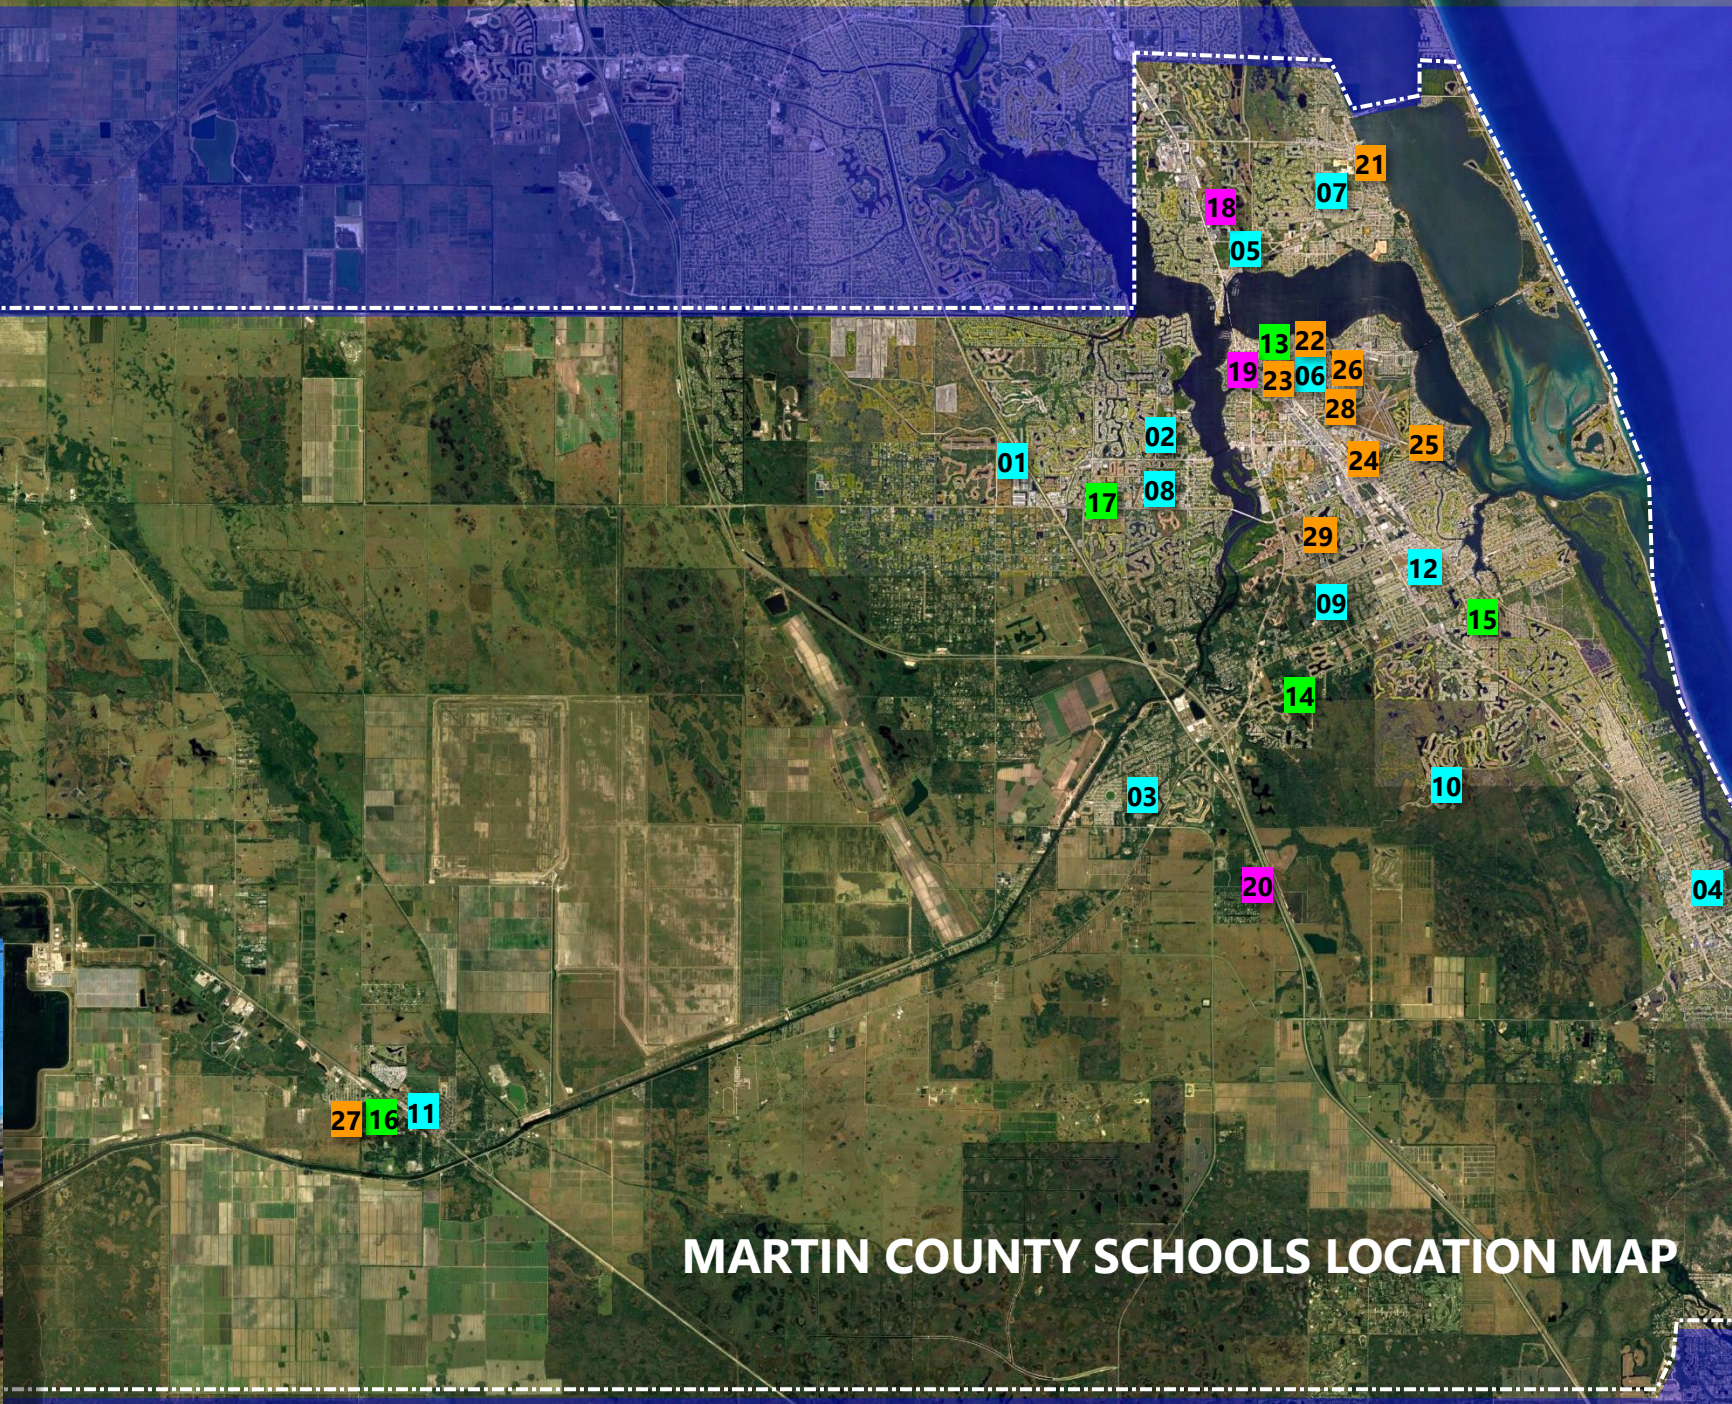

- 01 Citrus Grove Elementary
- 02 Bessey Creek Elementary
- 03 Crystal Lake Elementary
- 04 Hobe Sound Elementary
- 05 Felix A. Williams Elementary
- 06 J.D. Parker Elementary
- 07 Jensen Beach Elementary
- 08 Palm City Elementary
- 09 Pinewood Elementary
- 10 SeaWind Elementary
- 11 Warfield Elementary
- 12 Port Salerno Elementary
- 13 Stuart Middle
- 14 Anderson Middle
- 15 Murray Middle
- 16 Indiantown Middle
- 17 Hidden Oaks Middle
- 18 Jensen Beach High
- 19 Martin County High
- 20 South Fork High
- 21 Environmental Studies Center
- 22 Riverbend Academy
- 23 Spectrum Academy
- 24 Salerno Learning Center
- 25 Salerno Schoolhouse
- 26 Stuart Learning Center
- 27 Perkins Early Childhood Center
- 28 Stuart Adult Community High
- 29 Willoughby Learning Center

MARTIN COUNTY SCHOOLS LOCATION MAP

Elementary School

Middle School

High School

Special Centers

N

2

BESSEY CREEK ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

BESSEY CREEK ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CHILLER PROJECT IN PROCESS.



Live the vision. Achieve the mission.

CITRUS GROVE ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

CITRUS GROVE ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: LOBBY HARDENING PROJECT UNDER THE CONSTRUCTION PHASE.



Live the vision. Achieve the mission.

CRYSTAL LAKE ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

CRYSTAL LAKE ELEMENTARY SCHOOL

GUTTER REPLACEMENT PROJECT COMPLETE.



Live the vision. Achieve the mission.

FELIX A WILLIAMS ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

FELIX A WILLIAMS ELEMENTARY SCHOOL

GUTTER REPLACEMENT PROJECT COMPLETE



Live the vision. Achieve the mission.

HOBE SOUND ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

INDIANTOWN MIDDLE SCHOOL


ENHANCED SECURITY PROJECTS: LOBBY HARDENING PROJECT UNDER THE CONSTRUCTION PHASE.



Live the vision. Achieve the mission.

JD PARKER ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.

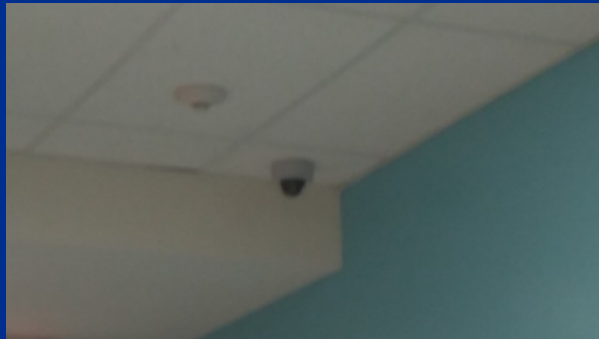

Live the vision. Achieve the mission.

JD PARKER ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: LOBBY HARDENING PROJECT
UNDER THE CONSTRUCTION PHASE.



Live the vision. Achieve the mission.

JD PARKER ELEMENTARY SCHOOL

CHILLER/REFURBISHING PROJECT COMPLETE.



Live the vision. Achieve the mission.

JD PARKER ELEMENTARY SCHOOL

GUTTER REPLACEMENT PROJECT COMPLETE.



Live the vision. Achieve the mission.

JENSEN BEACH ELEMENTARY SCHOOL


REPLACEMENT SCHOOL PROJECT- PROJECT SCHEDULE

- GMP BOARD APPROVAL **JULY 20, 2021**
- CONSTRUCTION PHASE – 719 DAYS
 1. Notice to Proceed Date: **JULY 27, 2021**
Construction Phase - **CURRENT PROJECT PHASE 3.7% COMPLETE**
 2. Calendar days from CMR notice to proceed to substantial completion of Phase 1:
479 Days (365 days + 114 days)- **NOVEMBER 18, 2022**
 3. Calendar days from CMR substantial completion of Phase 1 to substantial completion of both Phase 2 and 3: 251 Days- **JULY 27, 2023**
 4. Calendar days from CMR Phase 2 and 3 substantial completion to CMR final completion: 28 Days




JENSEN BEACH ELEMENTARY SCHOOL

REPLACEMENT SCHOOL PROJECT- PROGRESS

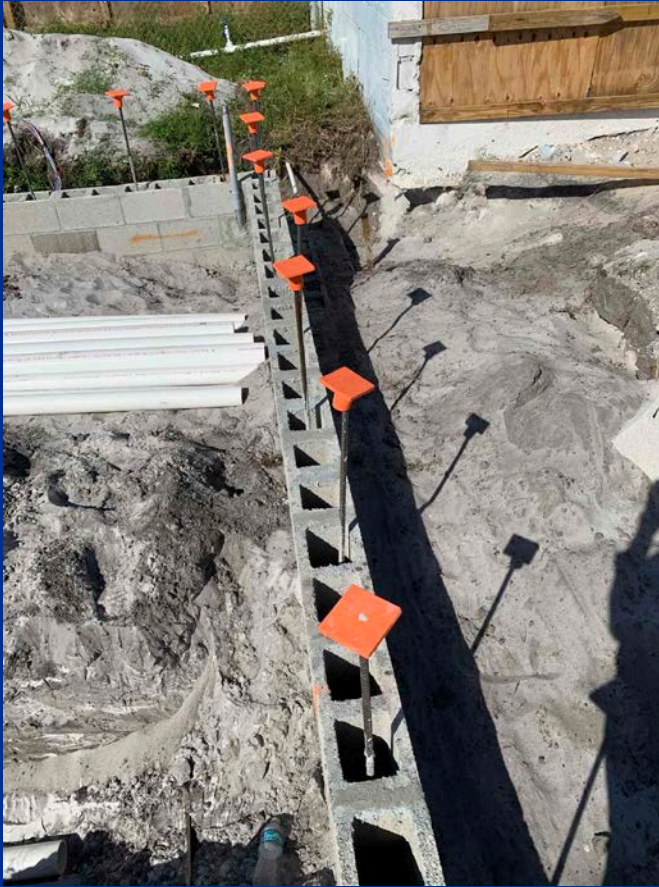

Live the vision. Achieve the mission.

JENSEN BEACH ELEMENTARY SCHOOL

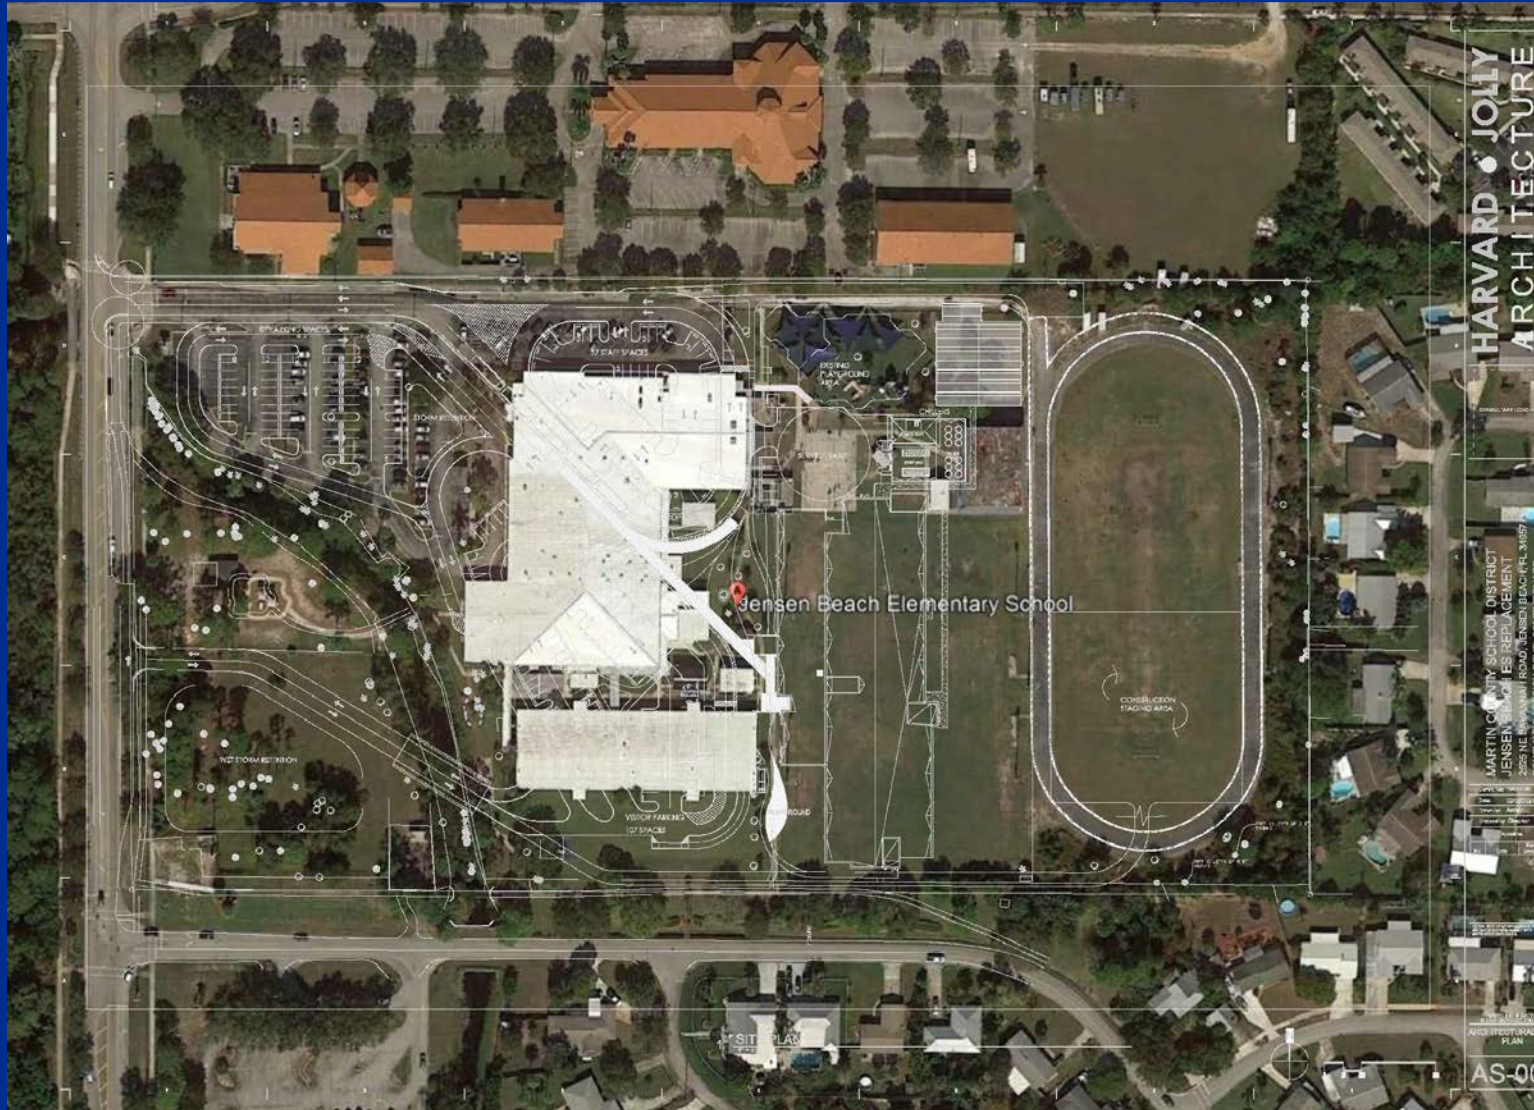

Live the vision. Achieve the mission.

PALM CITY ELEMENTARY SCHOOL

REPLACEMENT SCHOOL PROJECT- PROJECT SCHEDULE

- GMP BOARD APPROVAL JULY 20, 2021
- CONSTRUCTION PHASE – 719 DAYS
 1. Notice to Proceed Date: JULY 27, 2021
Construction Phase- **CURRENT PROJECT PHASE 5% COMPLETE**
 2. Calendar days from CMR notice to proceed to substantial completion:
479 Days (36 days + 114 days)- **NOVEMBER 18, 2022**
 3. Calendar days from CMR substantial completion to substantial completion of moving, demolition phase and site work: 150 Days- **APRIL 17, 2023**
 4. Calendar days from CMR completion of demolition phase & site work to CMR full completion: 90 Days



PALM CITY ELEMENTARY SCHOOL

REPLACEMENT SCHOOL PROJECT- PROGRESS



Live the vision. Achieve the mission.

PALM CITY ELEMENTARY SCHOOL



Live the vision. Achieve the mission.

PINEWOOD ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

PINEWOOD ELEMENTARY SCHOOL

WATER INTRUSION REPAIRS – GUTTERS PROJECT COMPLETE.



Live the vision. Achieve the mission.

PORT SALERNO ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

PORT SALERNO LEARNING CENTER

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

SEAWIND ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

WARFIELD ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

WARFIELD ELEMENTARY SCHOOL

ENHANCED SECURITY PROJECTS: LOBBY HARDENING PROJECT UNDER THE CONSTRUCTION PHASE.



Live the vision. Achieve the mission.

WILLOUGHBY LEARNING CENTER

ENHANCED SECURITY PROJECTS: CAMERA INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

WILLOUGHBY LEARNING CENTER

AIR HANDLER UNIT REPLACEMENT PROJECT COMPLETE.



Live the vision. Achieve the mission.

ANDERSON MIDDLE SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA UPDATE INSTALLATION COMPLETE.



Live the vision. Achieve the mission.

ANDERSON MIDDLE SCHOOL

AIR DAMPER AND CHILLER REBUILD PROJECT COMPLETE.



Live the vision. Achieve the mission.

ANDERSON MIDDLE SCHOOL

ROOF REPAIR BUILDING 4 COMPLETE.



Live the vision. Achieve the mission.

HIDDEN OAKS MIDDLE SCHOOL

COVERED WALKWAY EXTENSION COMPLETE.



Live the vision. Achieve the mission.

HIDDEN OAKS MIDDLE SCHOOL

ENHANCED SECURITY PROJECTS: CAMERA UPDATE IN PROCESS.
FENCE & GATE INSTALL ALMOST COMPLETE.



Live the vision. Achieve the mission.

INDIANTOWN MIDDLE SCHOOL


ENHANCED SECURITY PROJECTS: LOBBY HARDENING PROJECT UNDER THE CONSTRUCTION PHASE.



Live the vision. Achieve the mission.

STUART MIDDLE SCHOOL

NEW ADMINISTRATIVE & MEDIA CENTER BUILDING, NEW FOOD SERVICE AND MULTIPURPOSE BUILDING AND NEW POWER PLANT BUILDING PROJECT – GMP UNDER REVIEW & NEGOTIATIONS

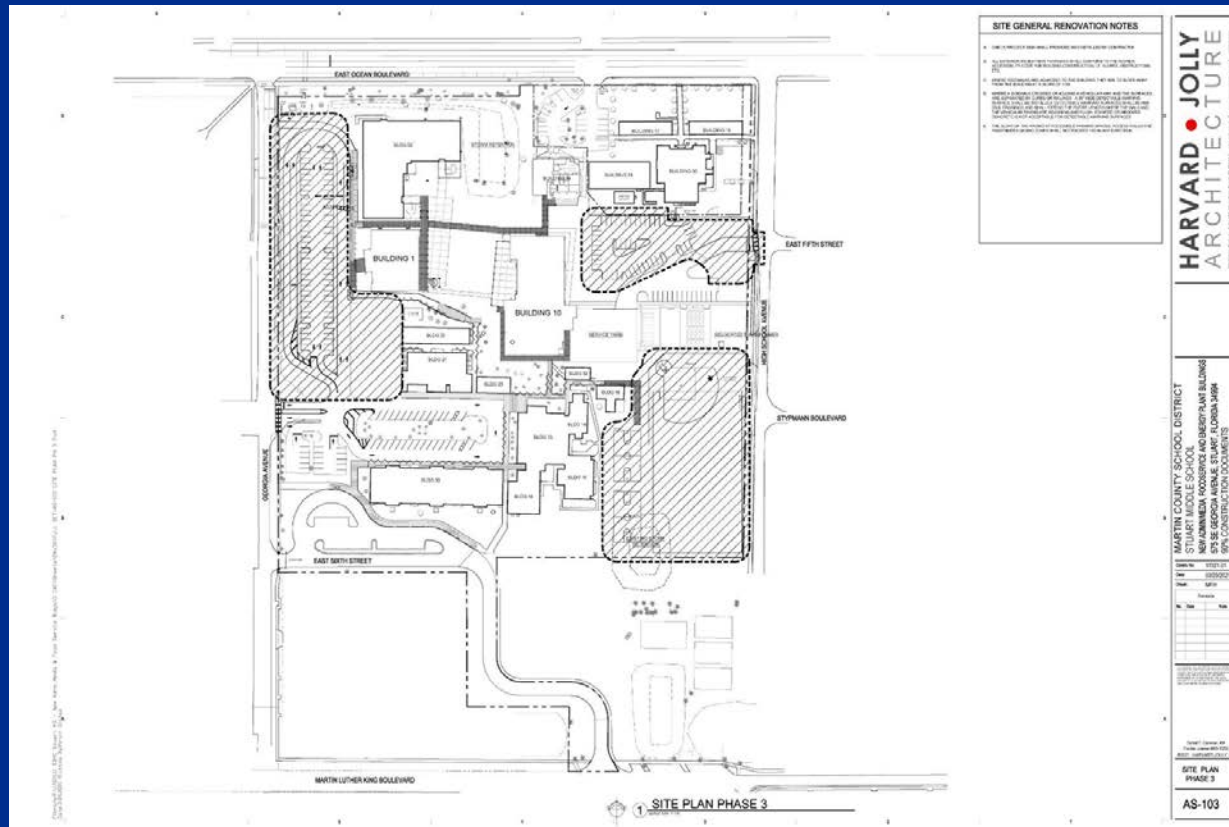

Live the vision. Achieve the mission.

JENSEN BEACH HIGH SCHOOL

ENHANCED SECURITY PROJECTS: FENCING & GATES PROJECT IN PROCESS.



Live the vision. Achieve the mission.

JENSEN BEACH HIGH SCHOOL


TENNIS COURT PROJECT COMPLETE.



Live the vision. Achieve the mission.

JENSEN BEACH HIGH SCHOOL


FLOORING REPLACEMENT PROJECT COMPLETE.

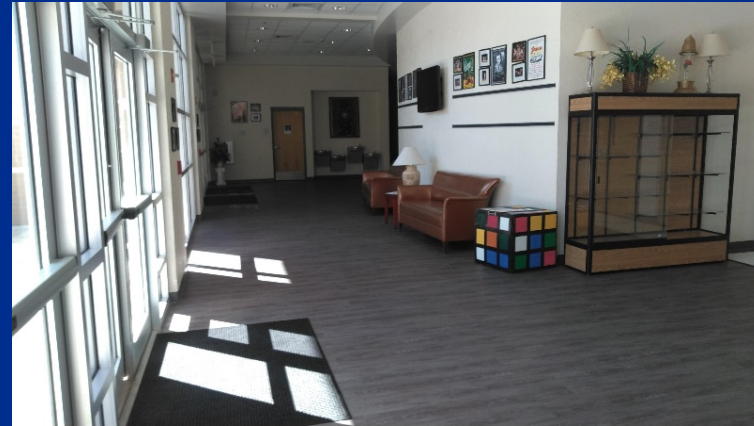

Live the vision. Achieve the mission.

JENSEN BEACH HIGH SCHOOL


ROOF REPLACEMENT PROJECT— BUILDING 6 WITH THE AUDITORIUM ROOF COMPLETE.

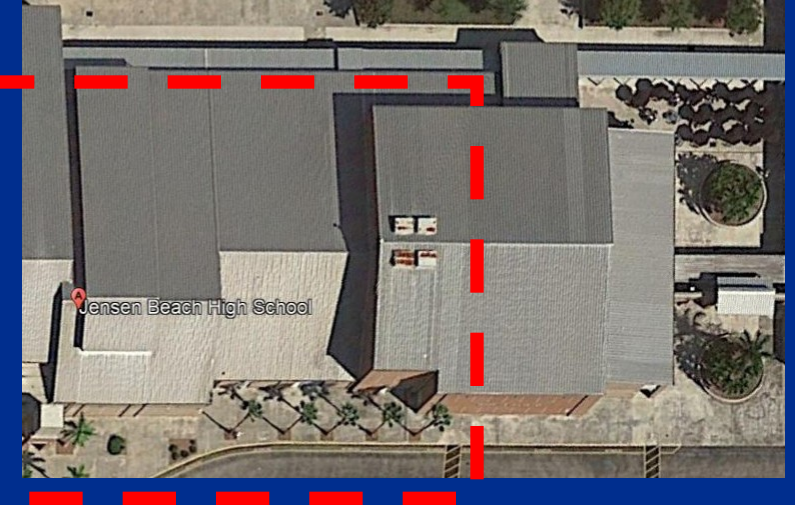

Live the vision. Achieve the mission.

JENSEN BEACH HIGH SCHOOL

ROOF REPLACEMENT PROJECT– DIFFERENT WATER INTRUSION PROJECTS
IN PROCESS ON SITE.

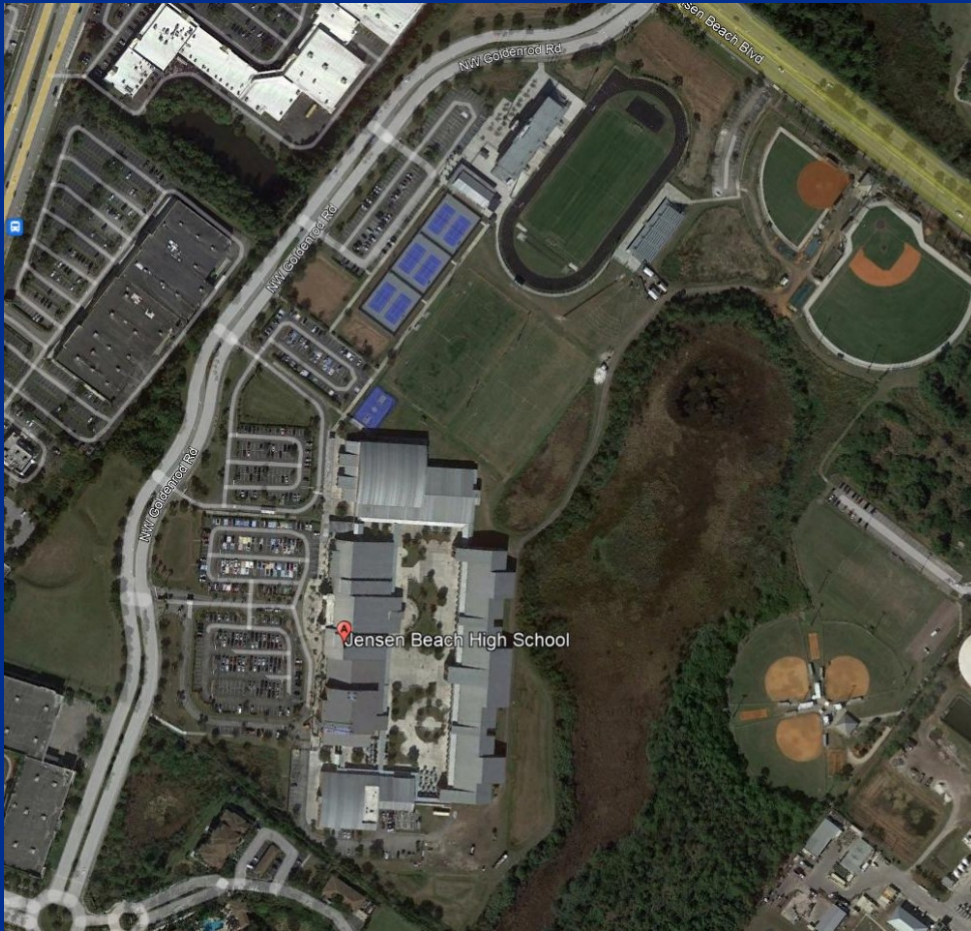

Live the vision. Achieve the mission.

MARTIN COUNTY HIGH SCHOOL


ENHANCED SECURITY PROJECT COMPLETE.



Live the vision. Achieve the mission.

SOUTH FORK HIGH SCHOOL


SPORTS COMPLEX & FIELDS, SITE DRAINAGE SYSTEM AND CHILLER PLANT & HVAC SYSTEM PROJECT – GMP PROCESS, Sub-Contractors Bidding Project

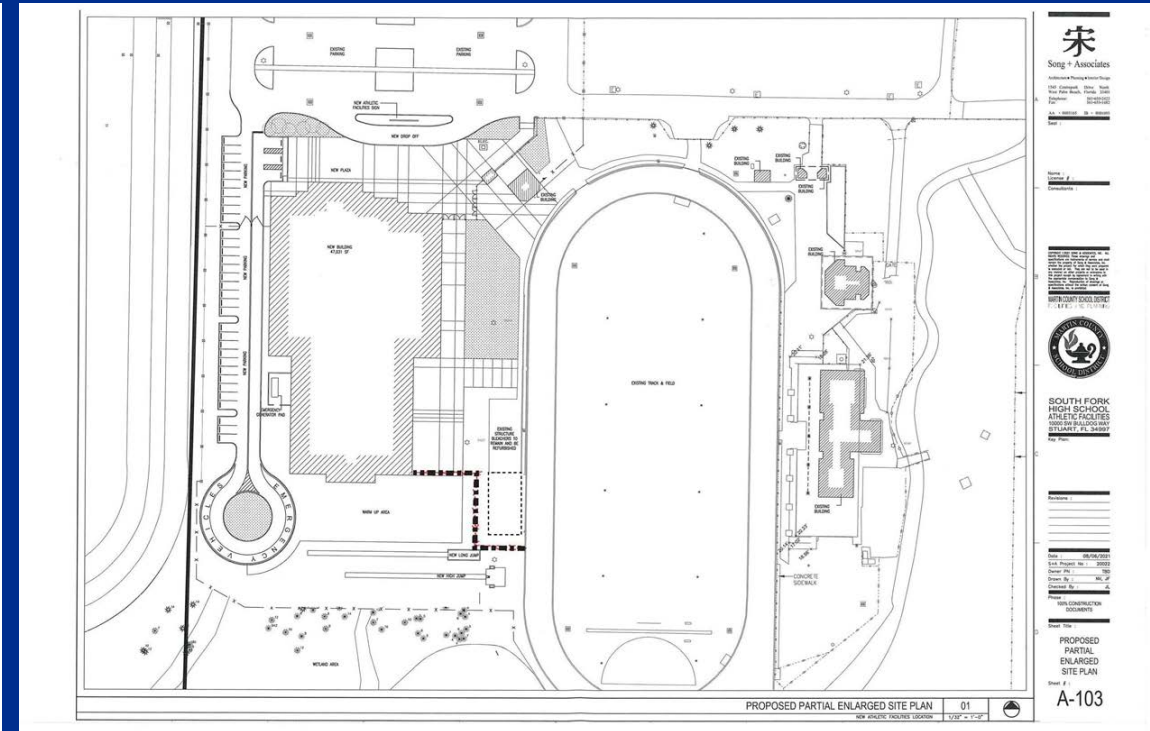

Live the vision. Achieve the mission.

STUART MIDDLE SCHOOL



NEW ADMINISTRATIVE & MEDIA CENTER BUILDING, NEW FOOD SERVICE AND MULTIPURPOSE BUILDING AND NEW POWER PLANT BUILDING PROJECT – GMP UNDER REVIEW & NEGOTIATIONS

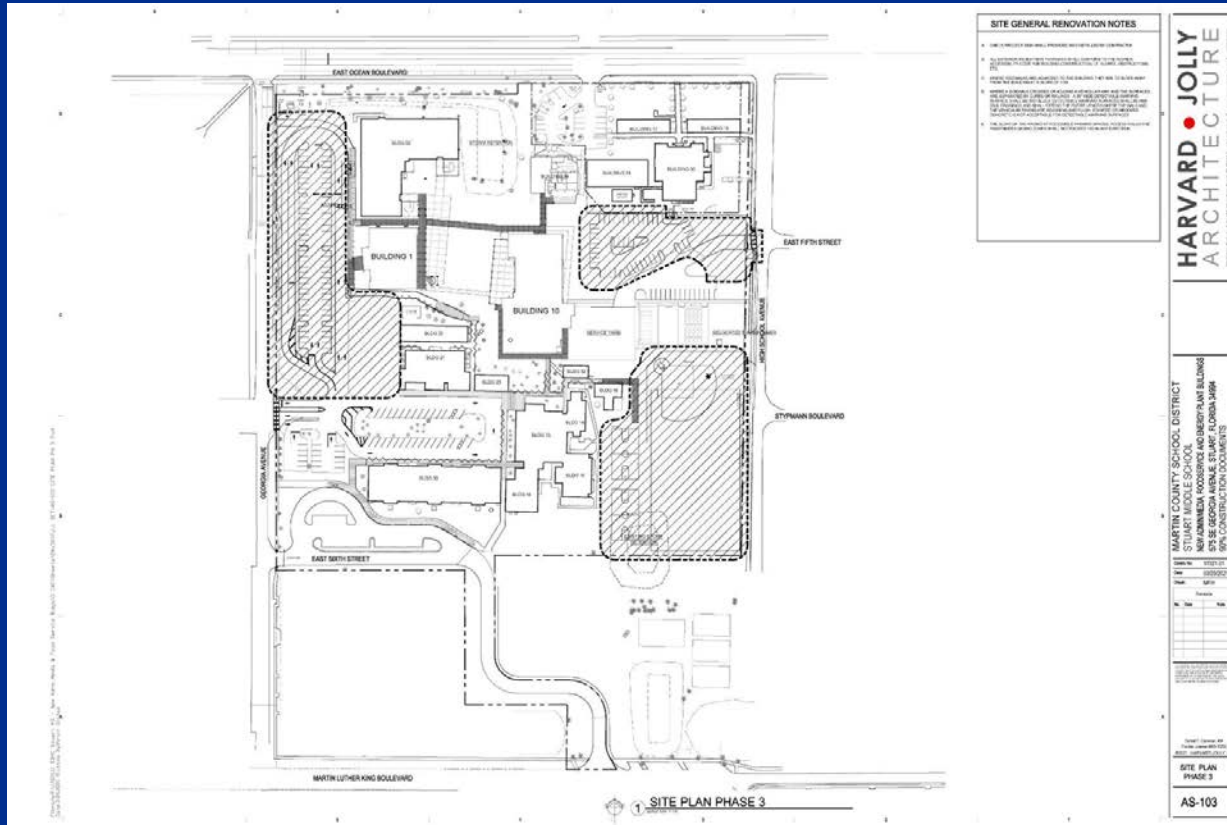

Live the vision. Achieve the mission.

SCHOOL DISTRICT OFFICE

NEW SDO BOARD ROOM , EXTERIOR FINISHES & ROOF PROJECT – ITB PUBLIC BID PROCESS, Bids Due 01-05-2022

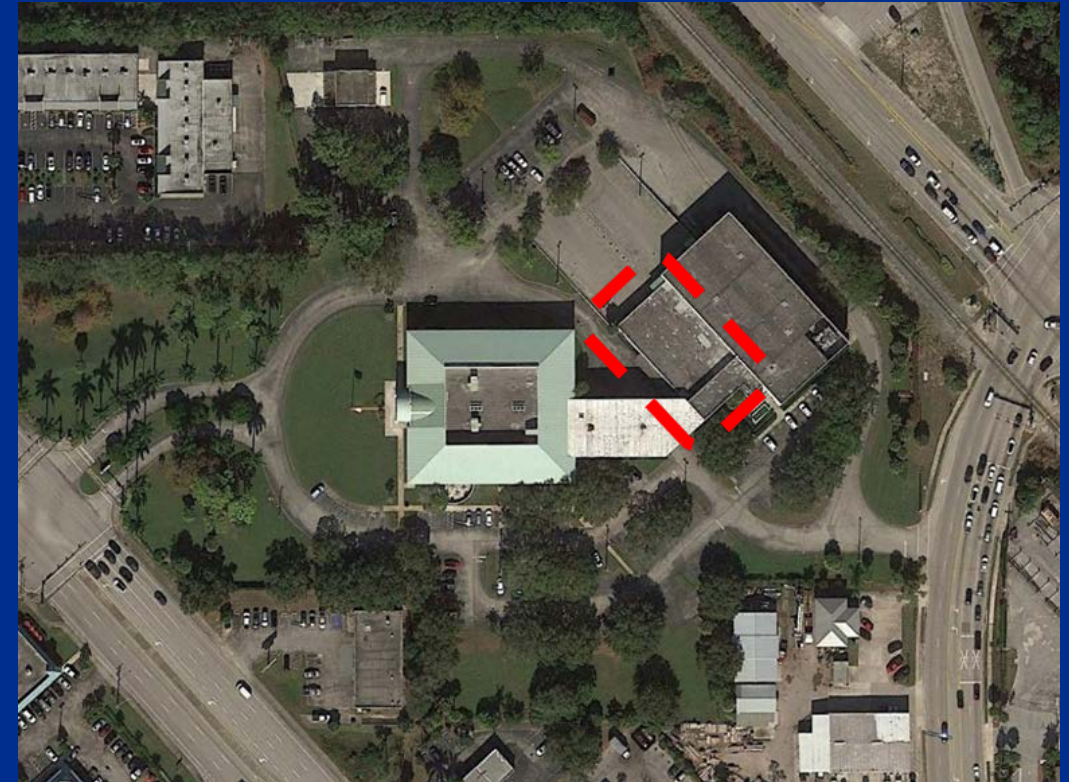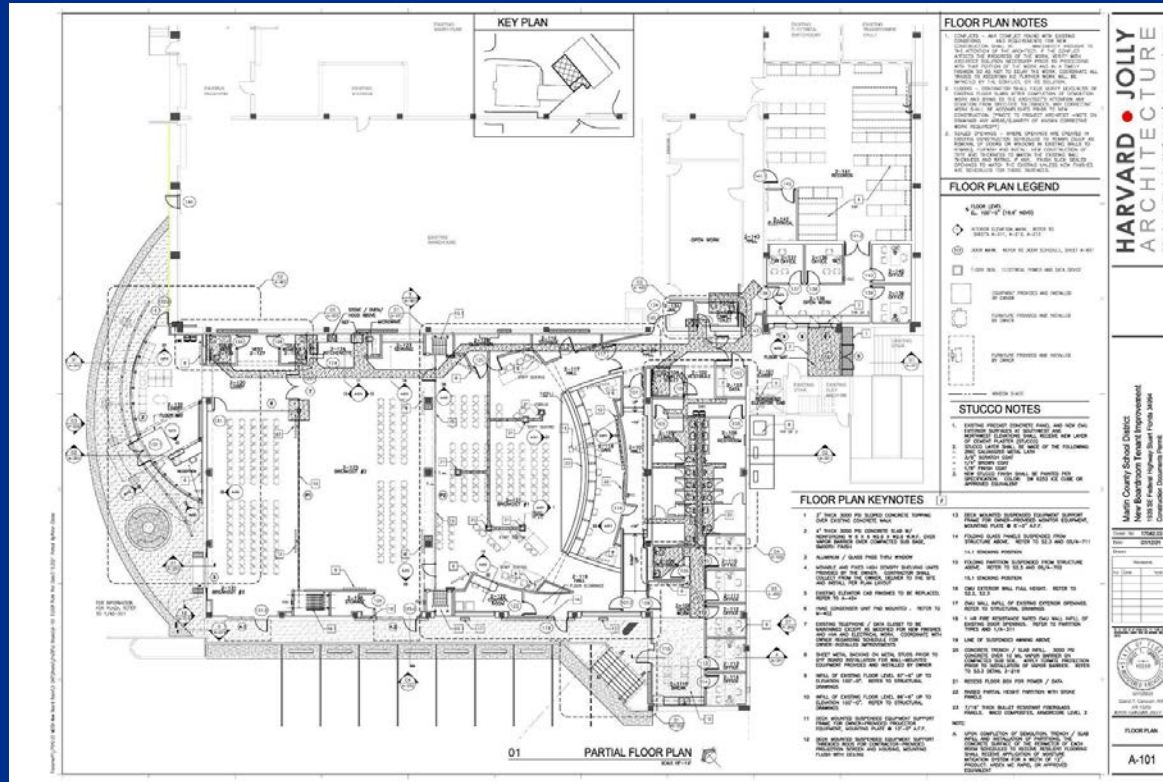

Live the vision. Achieve the mission.

PERKINS HEADSTART


ENHANCED SECURITY PROJECTS: CAMERA PROJECT COMPLETE.



Live the vision. Achieve the mission.

SALERNO SCHOOL HOUSE

ENHANCED SECURITY PROJECTS: CAMERA PROJECT IN PROCESS.

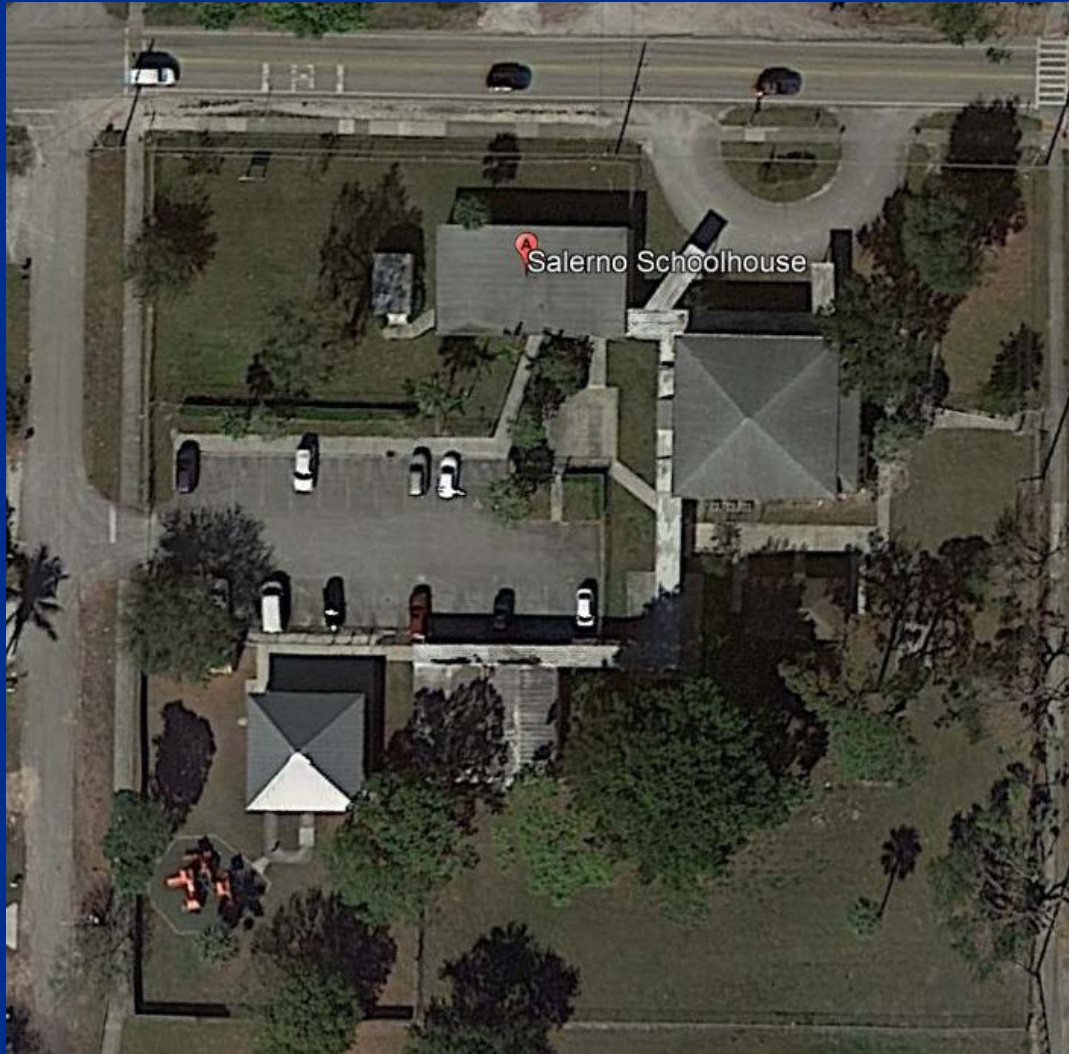

Live the vision. Achieve the mission.

ENVIRONMENTAL STUDIES CENTER

ENHANCED SECURITY PROJECTS: CAMERA PROJECT IN PROCESS.



Live the vision. Achieve the mission.

STUART LEARNING CENTER

ENHANCED SECURITY PROJECTS: CAMERA PROJECT IN PROCESS.



Live the vision. Achieve the mission.

PERKINS HEADSTART

ENHANCED SECURITY PROJECTS: CAMERA PROJECT IN PROCESS.



Live the vision. Achieve the mission.

TRANSPORTATION / MAINTENANCE / PURCHASING CENTER

ENHANCED SECURITY PROJECTS: CAMERA PROJECT INSTALL IN PROCESS.



Live the vision. Achieve the mission.

TRANSPORTATION / MAINTENANCE / PURCHASING CENTER

ENHANCED SECURITY PROJECTS: FENCING & GATES PROJECT
CONSTRUCTION DOCUMENTS IN PROCESS AND ALMOST COMPLETE.



Live the vision. Achieve the mission.

Mission:

- Educate all students for success
Martin County School

District Vision:

- A dynamic educational system of
excellence



THE END.



Live the vision. Achieve the mission.
