



**ISD #332**  
**New Mora High School**  
New 7-12 High School

ICS Weekly Progress  
Report  
Monday – May 15, 2023



Address: 200 N 9<sup>th</sup> St, Mora, MN, 55051

## Construction

- **Week ending May 12<sup>th</sup>, 2023**

- AJ Moore Electric continued electrical finishes and lighting in multiple areas.
- Mechanical finishes continued in multiple areas.
- Terrazzo finishing continued in the corridors.
- Ceiling grid installation continued in multiple areas.
- Painting, tile, and casework continued in multiple areas.
- Interior glass installation continued.
- Miscellaneous interior finishes continued in multiple areas.
- Exterior siding work continued.
- The bleacher installation in the gym began.
- Exterior concrete continued.
- The bleacher foundation was poured at the football field.
- Executive Touchpoint Meeting, Tuesday, May 9<sup>th</sup>, at 2:30 pm.
- Progress Meeting, Wednesday, May 10<sup>th</sup>, at 1:00 pm.

- **Week ending May 19<sup>th</sup>, 2023**

- Mechanical & electrical rough-ins and finishes will continue in multiple areas.
- Tile installation, painting, flooring, and ceiling work will continue in multiple areas.
- Sheetrock installation and taping will continue in multiple areas.
- Doors/Hardware and miscellaneous finishes will continue in multiple areas.
- Window/Interior glass work will continue in miscellaneous areas.
- Terrazzo finishing will continue in multiple areas.
- Exterior siding and coping work will continue.
- New Look to continue prepping the exterior site.
- Rigging, electrical, painting, and framing work will continue in the auditorium.
- Remodel work for the windows and west wall, will begin in the tow wellness center offices.
- Bleacher installation will continue in the gymnasium.
- Monthly Financial Review, Monday, May 15<sup>th</sup>, at 1:00 pm.
- Executive Touchpoint Meeting, Tuesday, May 16<sup>th</sup>, at 2:30 pm.
- Progress Meeting, Wednesday, May 17<sup>th</sup>, at 1:00 pm.

## Upcoming Important Dates

- **Complete Construction, summer of 2023.**


***Photo: Main entry sidewalk installation is ongoing.***



***Photo: The bleacher pad concrete foundation installed.***



***Photo: Bleacher installation in the gym.***

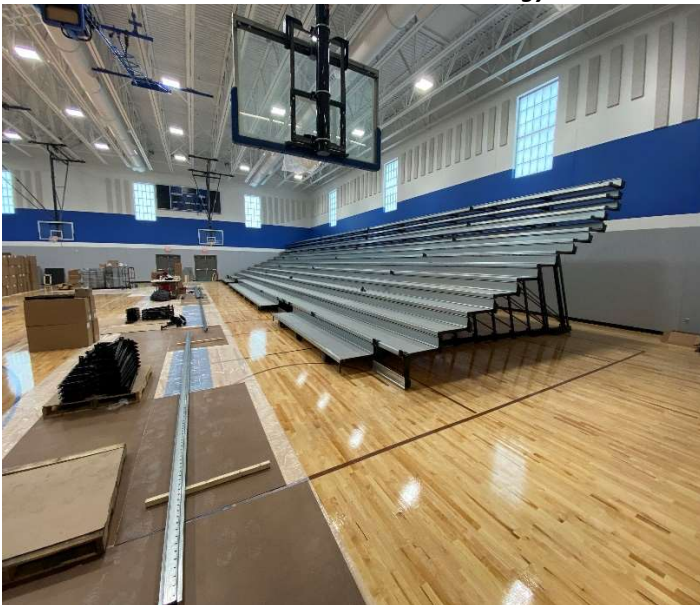

***Photo: Exterior siding completed at the classroom wings.***



***End of Update***
