



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Apollo Early Childhood Center**



Canopy Roof prepped and ready for Tectum Deck.



EPDM roofing installed on secured entry addition.



# HURON VALLEY SCHOOLS 2020 Bond Program


Bid Pack #5 - Construction Progress Update

5/31/22

## Apollo Early Childhood Center



Installation of damp proofing prepped for spray foam insulation.

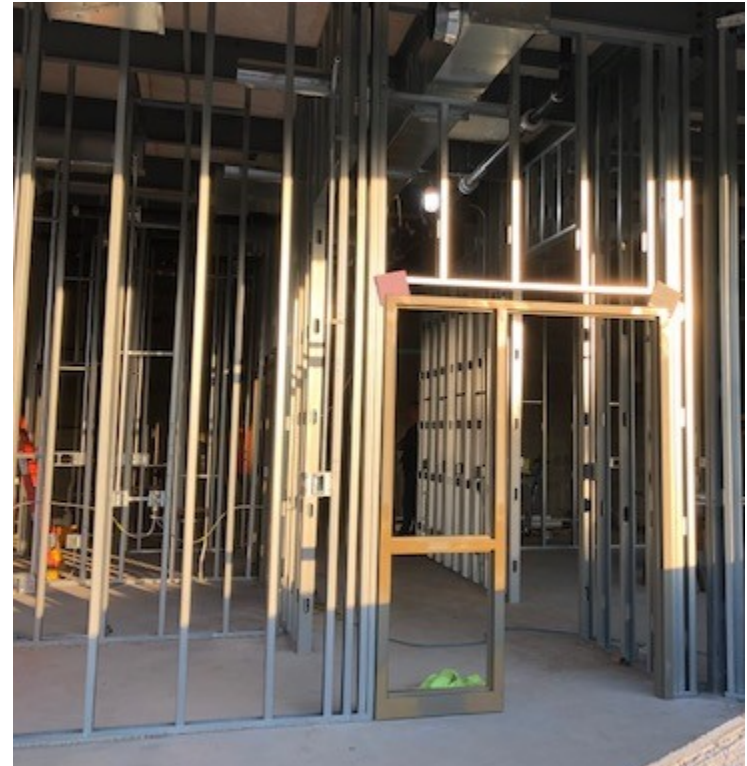

Interior metal studs and Hollow metal door frames installed



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Apollo Early Childhood Center**



HVAC duct work being installed



Toilet room concrete poured back and ready for CMU walls



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Country Oaks Elementary School**



Roof sumps and piping being installed



Spray foam insulation is completed in preparation for face brick at exterior walls and densglass installed.



# HURON VALLEY SCHOOLS 2020 Bond Program

Bid Pack #5 - Construction Progress Update

5/31/22

## Country Oaks Elementary School



Interior toilet room new sink carrier and rough plumbing installed



# HURON VALLEY SCHOOLS 2020 Bond Program

## Bid Pack #5 - Construction Progress Update

5/31/22

### Heritage Elementary School



Face brick laid at new addition and Densglass Sheathing put in place on exterior walls.




Wood blocking and sheathing installed in prep for metal panels.




**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Heritage Elementary School**

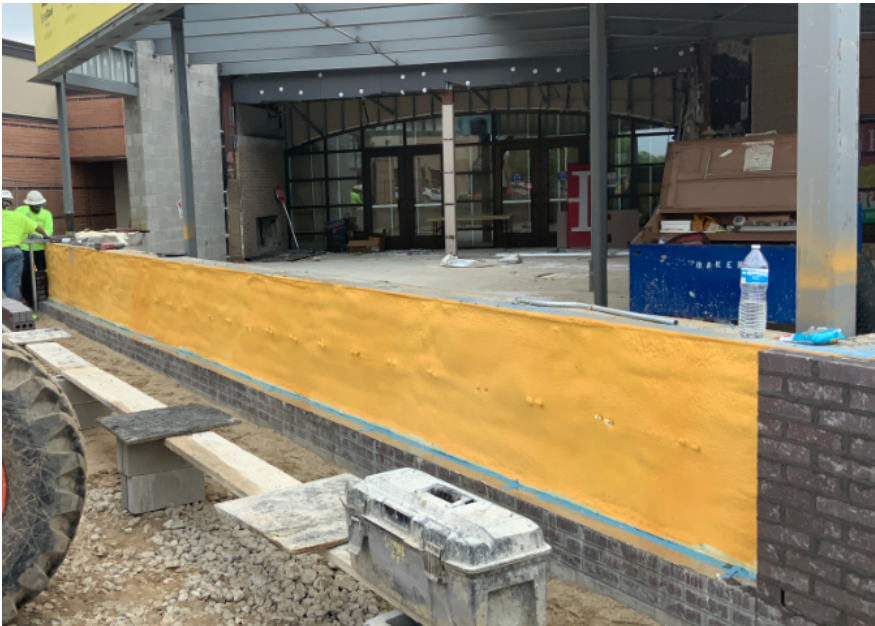

Spray foam insulation is completed in preparation  
for face brick at exterior walls

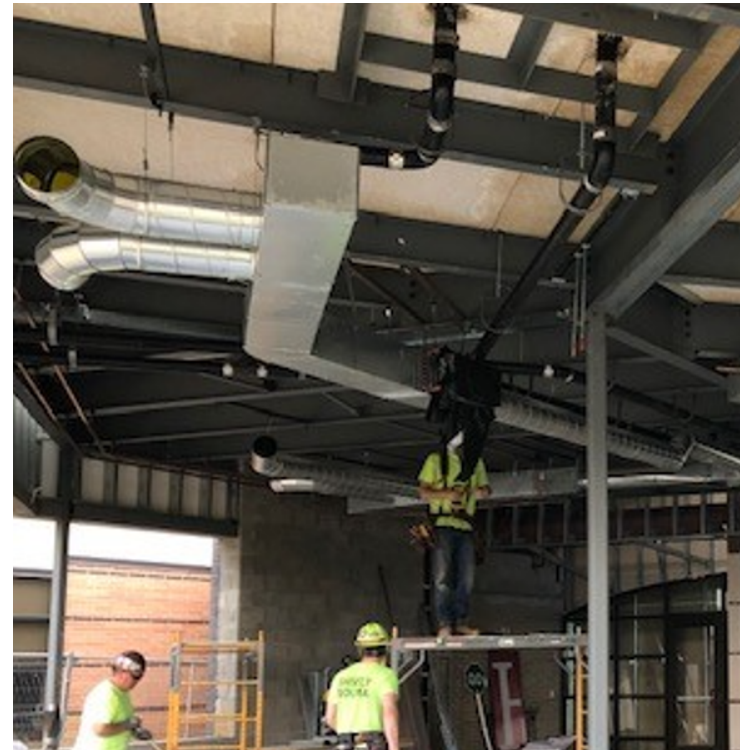

HVAC duct work being installed



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Kurtz Elementary School**



Curb for new RTU is Set and concrete in corridor poured




Face Brick laid at new addition





**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Kurtz Elementary School**

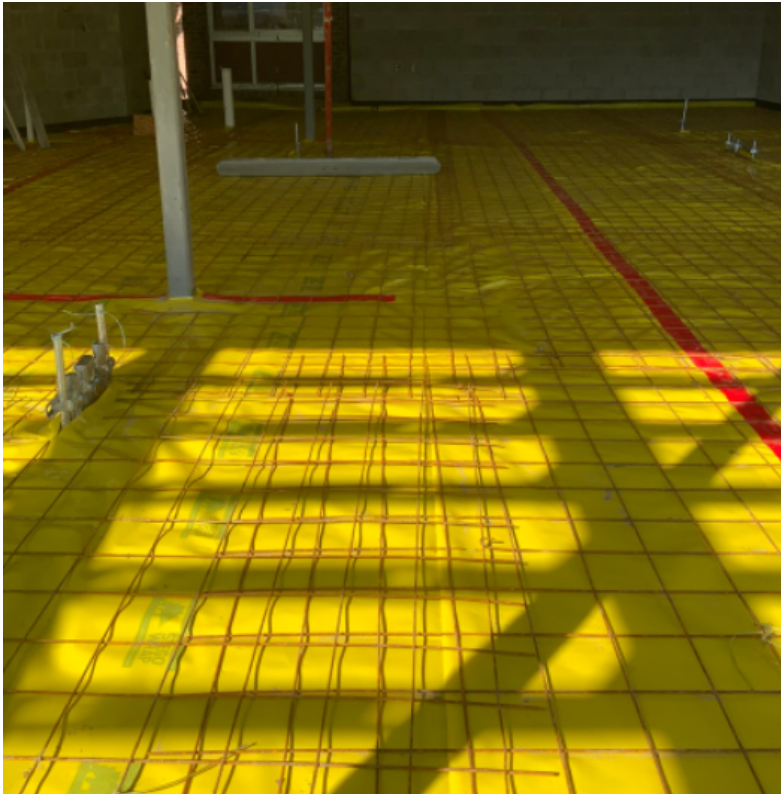

Vapor barrier and reinforcing steel are in place ahead of concrete floor slab pour



Concrete floor slab being poured and leveled in the Secured Entry Addition



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Kurtz Elementary School**



Slab on grade poured at secured entry addition




Roof sumps and piping being installed




**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Spring Mills Elementary School**

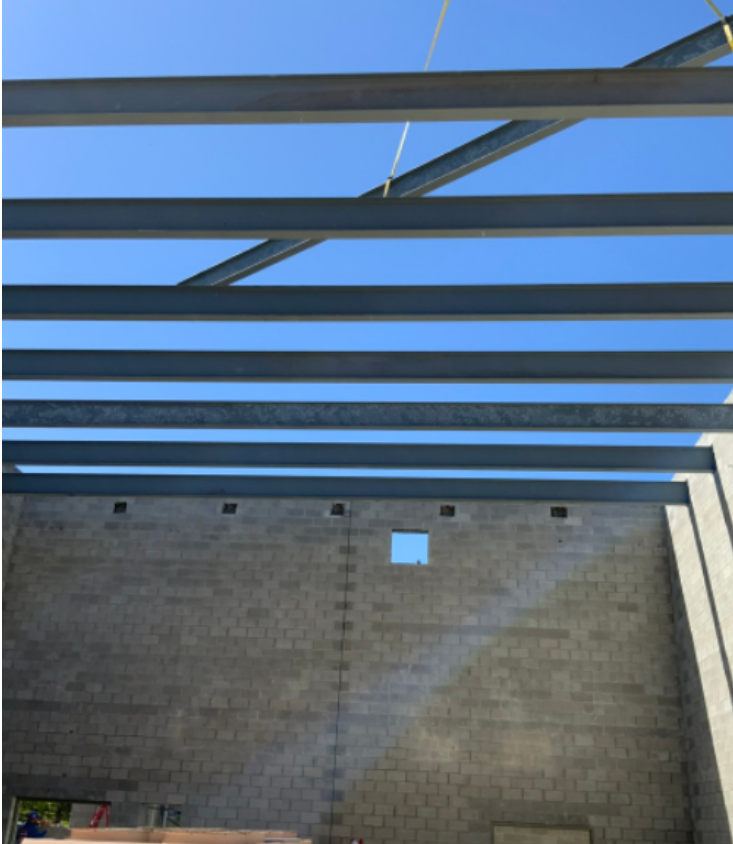

Structural Steel being set in place over the gymnasium.

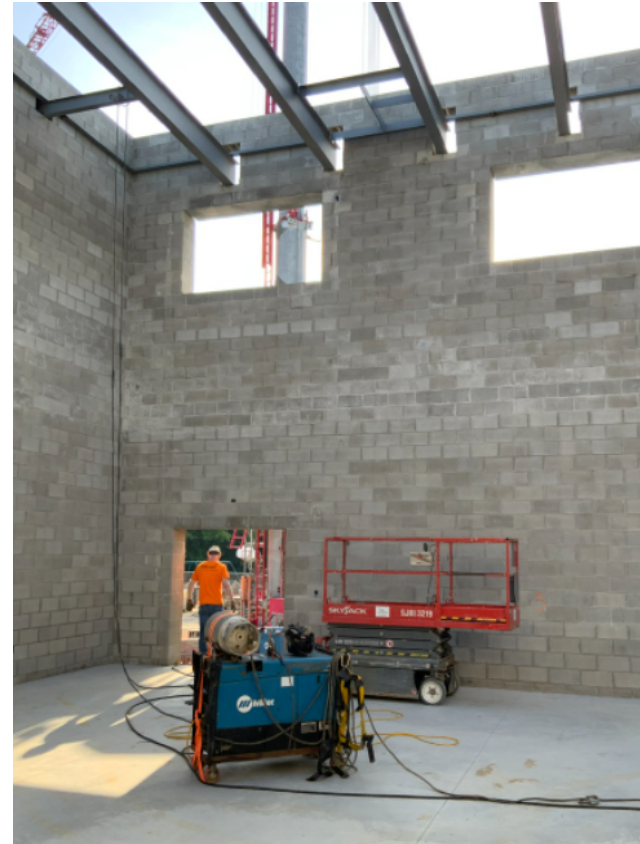

Structural Steel detailing throughout the addition



## HURON VALLEY SCHOOLS 2020 Bond Program

Bid Pack #5 - Construction Progress Update

5/31/22

### Spring Mills Elementary School



New equipment pad for new chiller poured



**HURON VALLEY SCHOOLS 2020 Bond Program**  
Bid Pack #5 - Construction Progress Update  
5/31/22

**Spring Mills Elementary School**



Electrical panel boxes installed, and equipment pad is ready for transformer



Above ceiling electrical rough in is on-going.
