


ALBION CENTRAL SCHOOLS Construction Phasing Site Plan	
<div> <div> <div></div> <div>Contractor Staging Area</div> </div> <div> <div></div> <div>Work Area</div> </div> <div> <div>HW</div> <div>Underground Hot Water Lines</div> </div> <div> <div></div> <div>Fence</div> </div> </div> <div>Legend</div>	
2023	<div> <div>1</div> <div>Football Field Replacement 04/3/23 - 09/1/23</div> </div> <div> <div>2</div> <div>Track Resurfacing 04/3/23 - 09/1/23</div> </div> <div> <div>3</div> <div>Multi-Purpose field replacement 06/1/23 - 07/15/24</div> </div> <div> <div>4</div> <div>Elementary School hot water service line 05/22/23 - 8/25/23</div> </div> <div> <div>5</div> <div>Elementary School drop-off loop & sidewalks 06/26/23 - 08/25/23</div> </div> <div> <div>6</div> <div>Replace Elementary School playground fence 06/26/23 - 08/25/23</div> </div> <div> <div>7</div> <div>High School hot water service line 05/22/23 - 08/25/23</div> </div>
2024	<div> <div>8</div> <div>Middle School hot water service (Alternate not selected)</div> </div> <div> <div>9</div> <div>Tennis court replacement 06/17/24 - 10/04/24</div> </div> <div> <div>10</div> <div>Middle School Drop-Off Loop reconstruction 06/24/24 - 08/30/24</div> </div> <div> <div>11</div> <div>Concrete sidewalk replacements 06/24/24 - 08/30/24</div> </div> <div> <div>12</div> <div>Playground Replacement 04/01/24 - 08/30/24</div> </div> <div> <div>13</div> <div>Baseball field drainage improvements 07/01/24 - 8/30/24</div> </div> <div> <div>14</div> <div>JV Softball field drainage improvements 7/01/24 - 8/30/24</div> </div>
<div> <div>*</div> <div>Refer to the full bid documents for all scopes of work and locations</div> </div>	

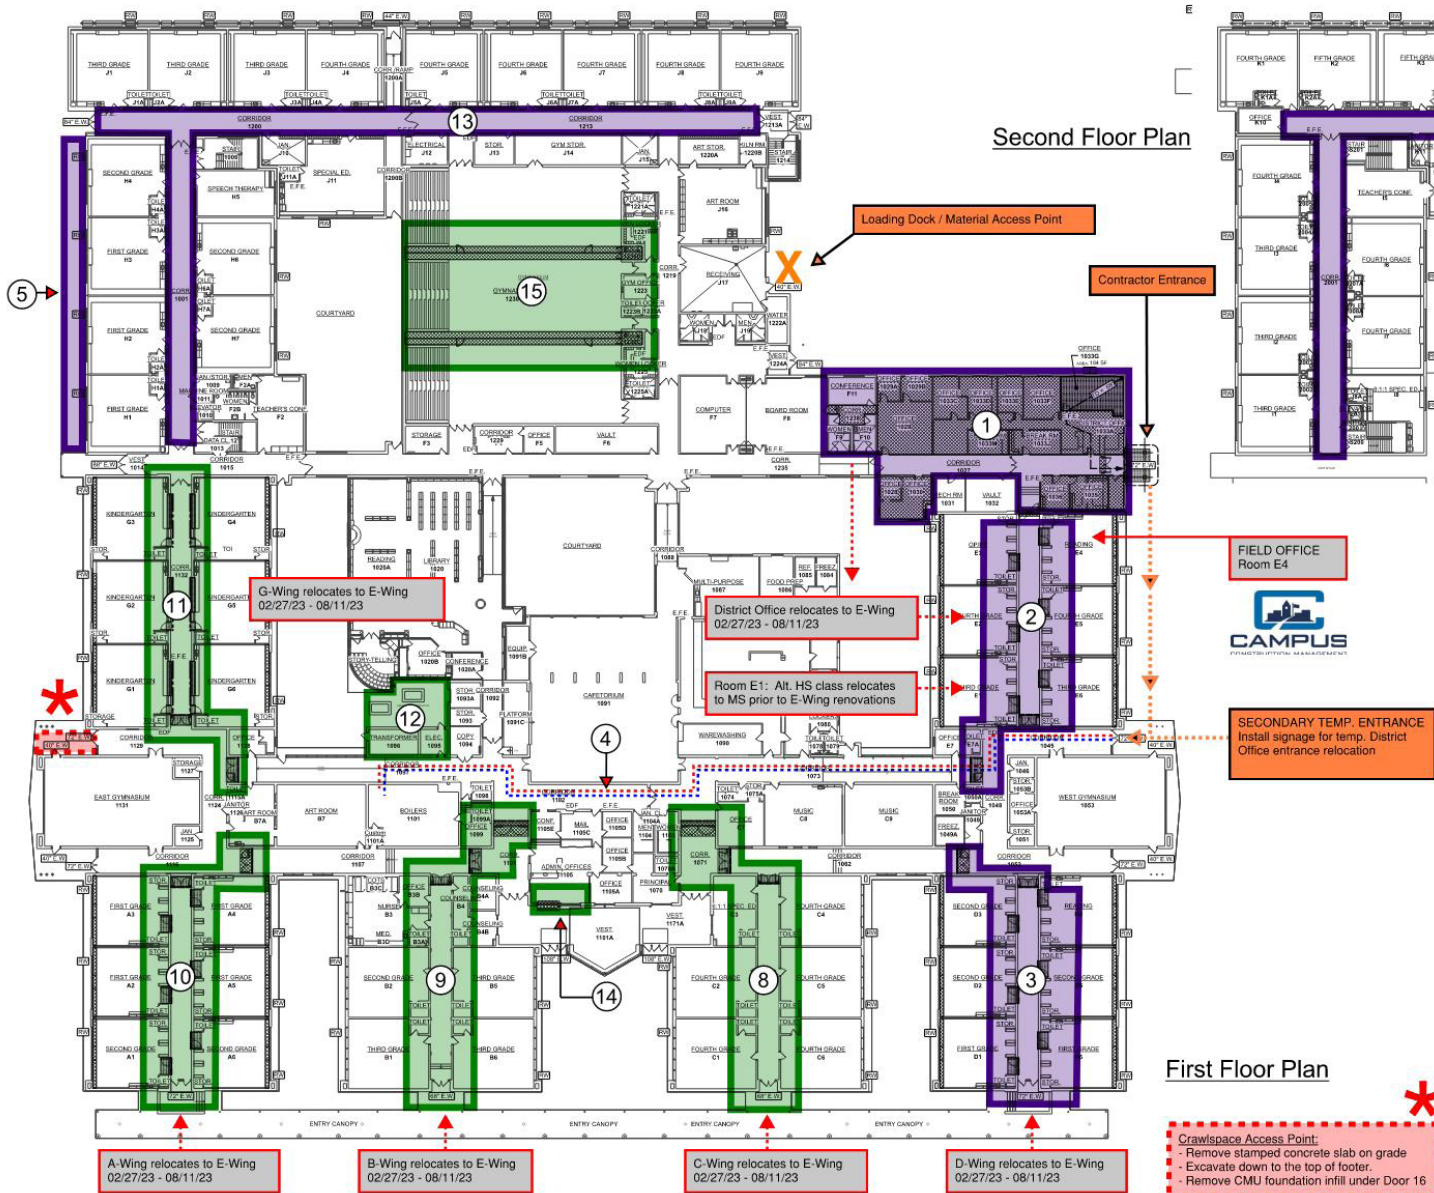

First Floor Plan

Crawspace Access Point:
 - Remove stamped concrete slab on grade
 - Excavate down to the top of footer.
 - Remove CMU foundation infill under Door 16

* Refer to the full bid documents for all scopes of work and locations

ALBION CENTRAL SCHOOLS Construction Phasing Plan Elementary School

2023

- ① District Office Renovation
03/06/23 - 08/11/23
- ② Classroom Doors & Plumbing Fixtures - E Wing
11/06/23 - 12/01/23
- ③ Classroom Doors & Plumbing Fixtures - D Wing
12/11/23 - 01/05/24
- ④ Crawl Space Plumbing & HW Heaters
06/27/23 - 12/29/23
- ⑤ EIFS Replacement
05/01/23 - 08/04/23
- ⑥ Carbon Monoxide Detectors / Fire Alarm
04/03/23 - 12/26/23
- ⑦ Electrical Abatement & Replacements
06/26/23 - 08/25/23

2024

- ⑧ Classroom Doors & Plumbing Fixtures - C Wing
01/15/24 - 02/09/24
- ⑨ Classroom Doors & Plumbing Fixtures - B Wing
02/19/24 - 03/15/24
- ⑩ Classroom Doors & Plumbing Fixtures - A Wing
03/25/24 - 04/19/24
- ⑪ Classroom Doors & Plumbing Fixtures - G Wing
04/29/24 - 05/24/24
- ⑫ Emergency Generator Replacement
04/01/24 - 07/26/24
- ⑬ Doors / Hardware / Security Enhancements
01/24/24 - 08/30/24
- ⑭ Main Office Windows & Fire Shutter
05/01/24 - 08/30/24
- ⑮ Gymnasium Folding Partition Replacement (Alt. #1)
04/15/24 - 08/30/24

ALBION CENTRAL SCHOOLS

Construction Phasing Plan

Middle School - Basement


2023

- ① Pool Deck Structural Repairs
04/28/23 - 10/06/23
- ② Boiler Room Abatement / Demo
06/26/23 - 08/11/23
- ③ Boiler Room Plumbing Renovations
08/14/23 - 09/08/23
- ④ Pool Pumps
09/04/23 - 10/20/23


2024

- ⑤ Electrical Room A/C
06/22/24 - 08/23/24
- ⑥ Auditorium A/C
06/22/24 - 08/23/24

* Refer to the full bid documents for all scopes of work and locations

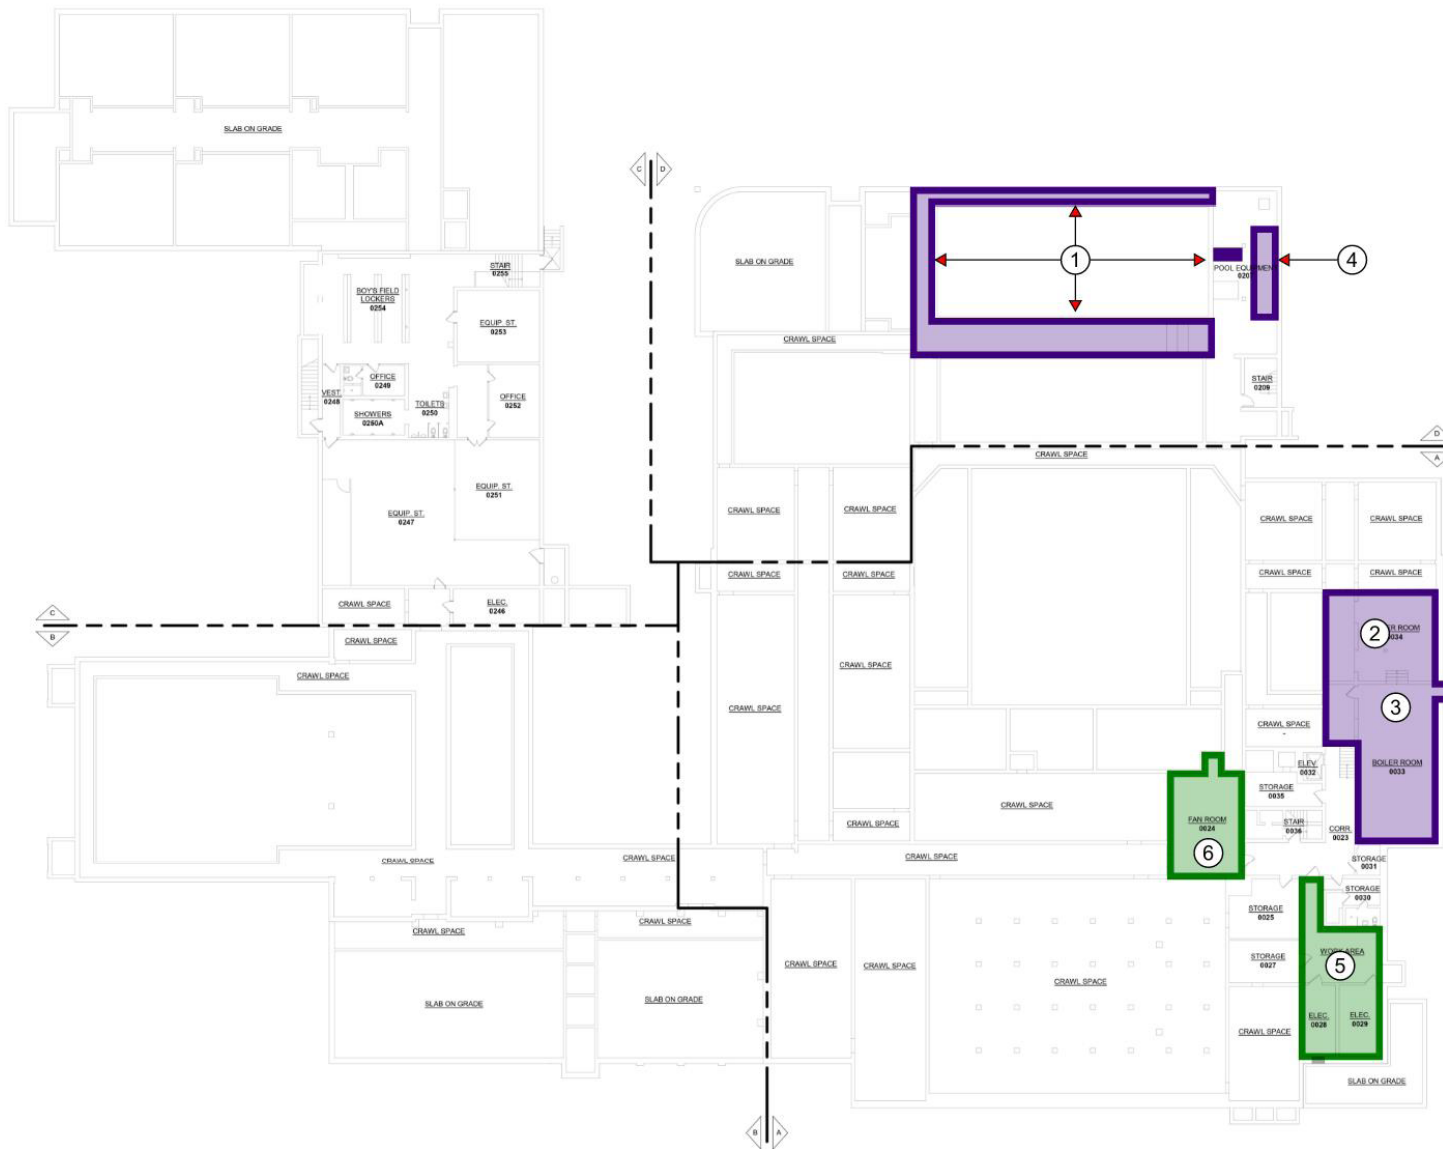

BASEMENT FLOOR PLAN

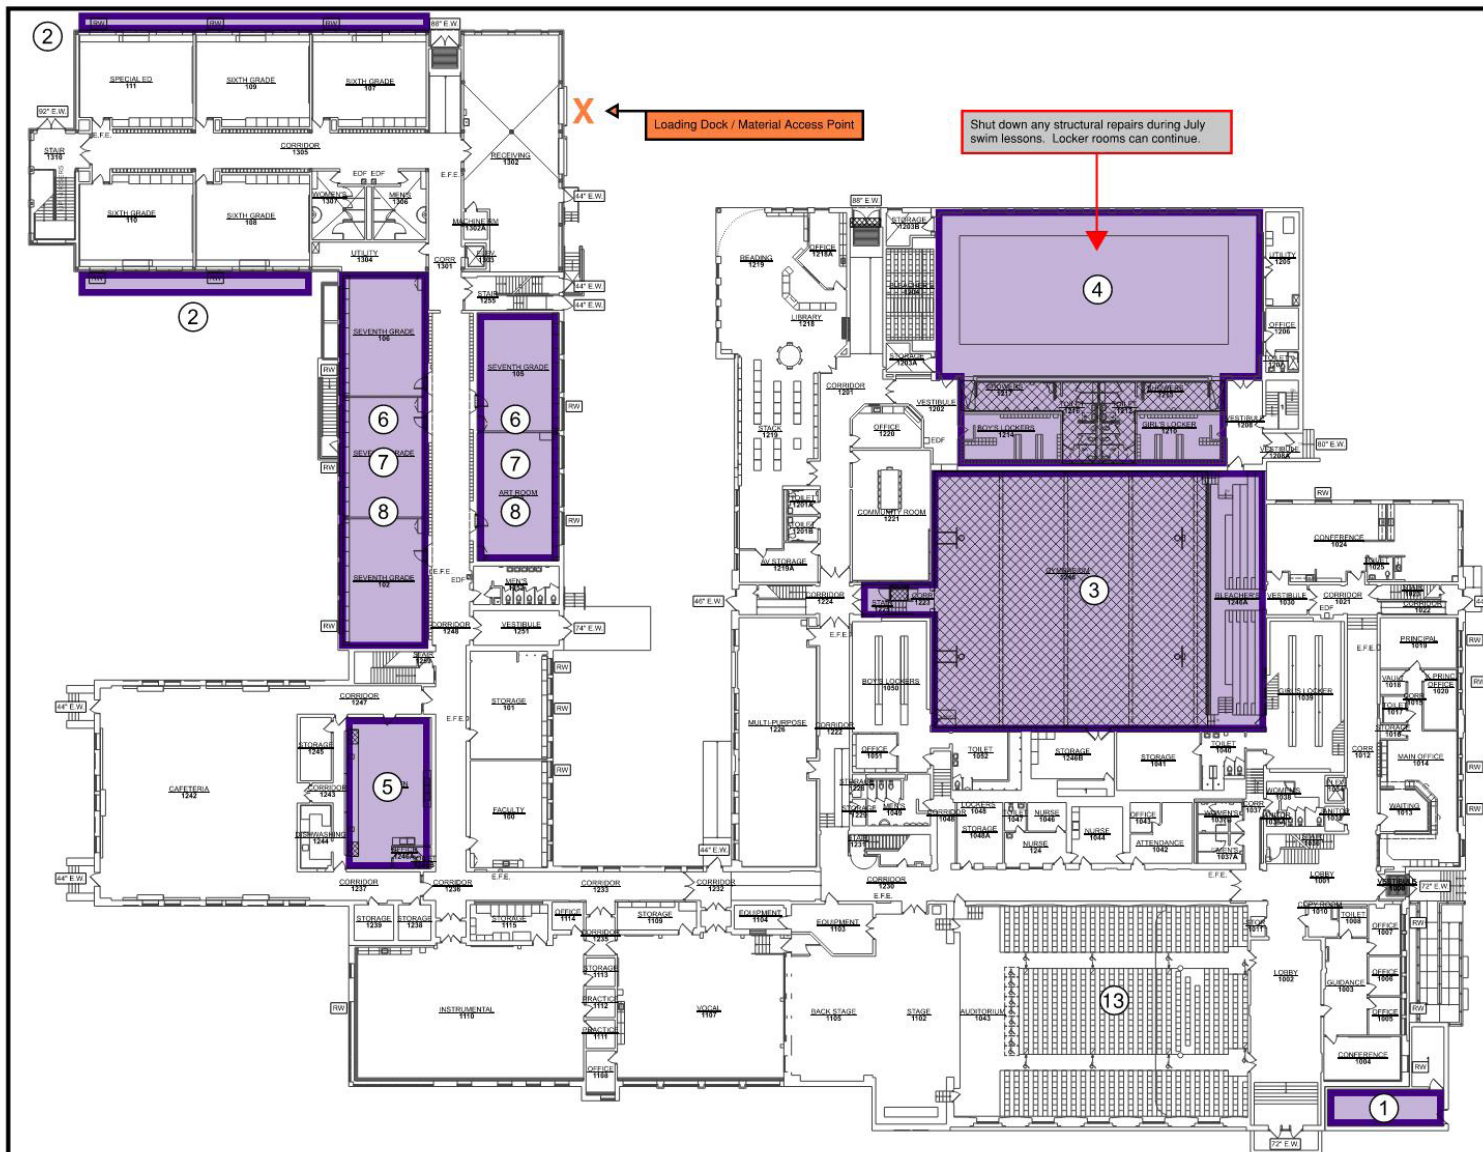

First Floor Plan

ALBION CENTRAL SCHOOLS

Construction Phasing Plan Middle School

2023

- ① Domestic Hot Water Repairs
03/17/23 - 04/21/23
- ② Replace insulated window panels
06/06/23 - 08/04/23
- ③ Gymnasium Renovations
04/28/23 - 09/01/23
- ④ Pool Lighting & Locker Room Renovation
04/28/23 - 10/06/23
- ⑤ Replace ANSUL System
06/26/23 - 08/25/23
- ⑥ Exhaust Fan & Relief Air work
06/26/23 - 09/01/23
- ⑦ Flooring Abatement
06/26/23 - 07/14/23
- ⑧ Flooring Installation
07/17/23 - 09/01/23
- ⑨ Carbon Monoxide Detectors / Fire Alarm
05/01/23 - 01/12/24
- ⑩ Electrical Service Component Replacements
05/22/23 - 12/28/23

2024

- ⑫ Doors / Hardware / Security Enhancements
03/04/24 - 08/30/24
- ⑬ Auditorium AC
05/27/24 - 08/30/24

★ Refer to the full bid documents for all scopes of work and locations

ALBION CENTRAL SCHOOLS Construction Phasing Plan Middle School - Third Floor


2023

- ① Exhaust Fan & Relief Air work
06/26/23 - 09/01/23

2024

- ② Doors / Hardware / Security Enhancements
03/04/24 - 08/30/24

* Refer to the full bid documents for all scopes of work and locations

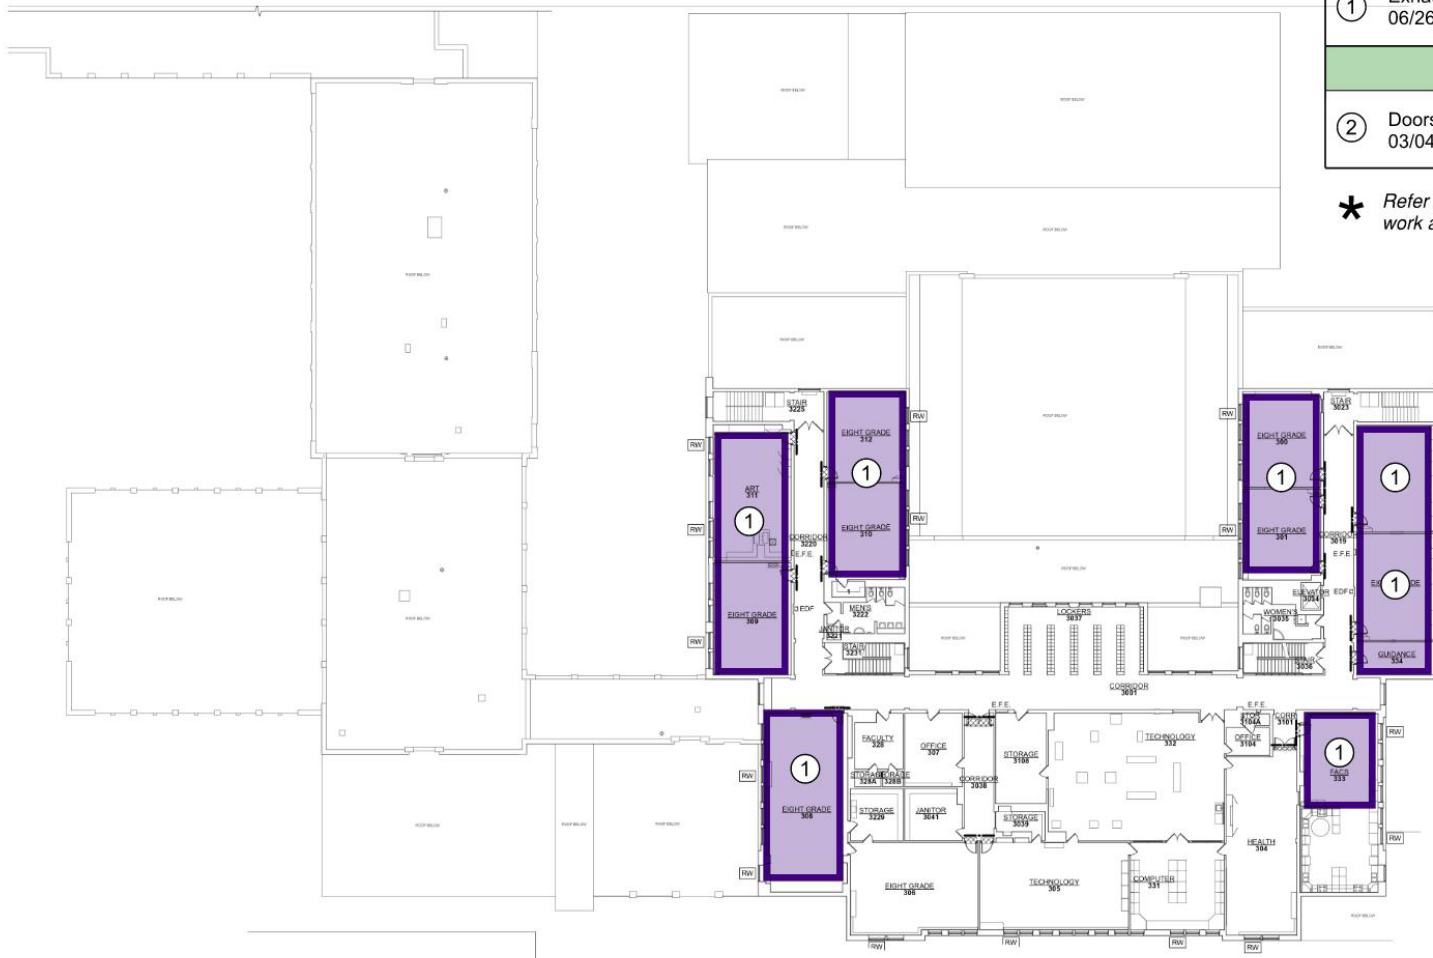

THIRD FLOOR PLAN

ALBION CENTRAL SCHOOLS Construction Phasing Plan High School

2023

- ① Library Door Reconstruction
06/26/23 - 08/25/23
- ② Window Lintel Replacements
05/29/23 - 08/25/23
- ③ Domestic Hot Water Heaters
06/26/23 - 08/25/23
- ④ Carbon Monoxide Detectors / Fire Alarm
05/22/23 - 01/12/24

2024

- ⑤ Replace Lockers
06/24/24 - 08/30/24
- ⑥ Not Used
- ⑦ Doors / Hardware /Security Upgrades
04/08/24 - 08/30/24
- ⑧ Gym Renovations
04/03/24 - 08/31/24
- ⑨ Gym Locker Room Renovations
04/22/24 - 12/13/24

* Refer to the full bid documents for all scopes of work and locations



First Floor Plan

ALBION CENTRAL SCHOOLS Construction Phasing Plan High School

2023

- ① Library Door Reconstruction
06/26/23 - 08/25/23
- ② Window Lintel Replacements
05/29/23 - 08/25/23
- ③ Domestic Hot Water Heaters
06/26/23 - 08/25/23
- ④ Carbon Monoxide Detectors / Fire Alarm
05/22/23 - 01/12/24

2024

- ⑤ Replace Lockers
06/24/24 - 08/30/24
- ⑥ Not Used
- ⑦ Doors / Hardware / Security Upgrades
04/08/24 - 08/30/24
- ⑧ Gym Renovations
04/03/24 - 08/31/24
- ⑨ Gym Locker Room Renovations
04/22/24 - 12/13/24
- ⑩ Gym HVAC Abatement & Demo.
05/24/24 - 07/24/24
- ⑪ Gym HVAC Installation
07/08/24 - 08/30/24

* Refer to the full bid documents for all scopes of work and locations





GRASS TURF REPLACEMENTS

- 1 – TRACK AND FOOTBALL FIELD
- 2 – MULTI-PURPOSE FIELD
 - SOCCER
 - SOFTBALL FIELD
- 3 – NEW CONCRETE SIDEWALKS

