

MILAN C-2 SCHOOL DISTRICT

BETTER MC2 – PROJECT 2020
JUNE 2020 Community Update



June 7th, 2020

NEW CONSTRUCTION UPDATE –

The project is making some very visible improvements. The masonry blocks are approaching full completion around the new KITCHEN and bathrooms. They have then started on the south wall of the new gym (that separates the gym and cafeteria-commons area).



This is an 'above' perspective of the Kitchen – the three (3) windows are on the south side of the kitchen. The Bar Joists for the roof/ceiling are also installed.



This is an extended view of the Cafeteria-Commons Area. The masonry blocks are being installed to the gym wall.

This a MARKET STREET perspective of the Kitchen/Commons Area



Striving for Excellence in Everything

MILAN C-2 SCHOOL DISTRICT

BETTER MC2 – PROJECT 2020

JUNE 2020 Community Update



RENOVATION UPDATE –

There are multiple areas within the campus that are to be renovated – the elementary (to absorb the 5th and 6th grade classes), the former cafeteria to be transitioned to a Library-Media Center, the former and separated Modular Building to be transitioned to the Central Office.



This is the former 4th grade hall, but after completion, this will be the 5th/6th grade section and the lockers were installed to support those students.

This was formerly a classroom in the Modular, but will serve as the new MC2 Board of Education room/office.




This is a former classroom, that has had a wall installed to provide a new Bookkeeper's Office and a work area for various needs.

MILAN C-2 SCHOOL DISTRICT

BETTER MC2 – PROJECT 2020
JUNE 2020 Community Update



This is the new door frame area for the Central Office, will be completed with a secure electronic entry (similar to other offices on campus)

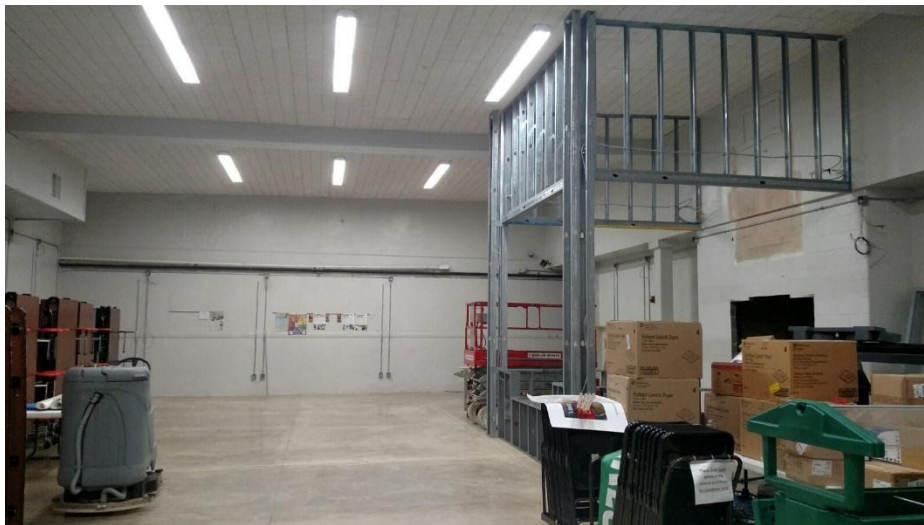

The above picture shows the beginnings of the new Library-Media Center (LMC) – the large floor-to-ceiling metal frame is the new LMC Specialist's reception desk.

JUNE 2020 Summary

As soon as the Central office is moved out of the existing Elementary building – the renovations will begin on the Elementary. The specific Elementary renovations consist of relocated offices for the Elementary Principal and Elementary Administrative Assistant, plus the removal of seven (7) walls to provide large-full size classrooms in the west Elementary hallway.

On or around June 15th, the base floor for the competitive gymnasium will be poured. The further completion of the ceiling/roof of the Cafeteria/Commons Area and Kitchen will greatly enhance the completion of the various details – as the weather will not be a factor.

Striving for Excellence in Everything

MILAN C-2 SCHOOL DISTRICT

BETTER MC2 – PROJECT 2020

JUNE 2020 Community Update



The timeline priority is the Cafeteria/Commons Area, Kitchen, Library-Media Center, Elementary and Modular renovations – as all of these tasks must be completed prior to 9/8/20. The New Gym, Locker Room and the Weight-Training room are to be completed by November, 2020.

Contact Ben Yocom – 660-265-4414 Ext. 1 or via email at byocom@milan.k12.mo.us.
